

Portfolio Sample - Weekly Progress Dashboard

Project Controls (Planning / Cost / Reporting)

Power BI | Primavera P6 | EVM



Prepared by: Eng. Obieda Omari | Portfolio Sample | Confidential

Phases

O.C

O.ENG.AR.A

O.ENG.AR.S

O.PROC.AR.S

MockUP Status

100%

50%

100%

100%

100%

100%

100%

100%

100%

100%

100%

Clinic - GF ID1...

Corridor - In fr...

ER Treat...

ICU - L02 M...

LDR - ID163...

Nurse Statio...

Patient Room ...

Physiot... Treat...

Renal Dialysi...

Waiting L03 - I...

● Max of SCH.%

● Max of PERF.%

MockUp Names

Select all

Clinic - GF ID1621B

Corridor - In front of Patient Room

ER Treatment GF-03 - ER-GR-46 - ID1623B

ICU - L02 MEQ 406

LDR - ID1630B-L03

Nurse Station - L04 ID1634A & B

Patient Room with Toilet - L04 - 057 and L04 - 056

Physiotherapy Treatment FF-L01-026 - ME...

Renal Dialysis Treatment L01-011-ID1625B

Waiting L03 - ID1631B

Mockup Status

30%

70%

● Completed

● In-Progress

● Not-Started

Material Code By Discipline

ARCHETICTURAL/ STRUCTURAL (%)

ELECTRICAL (%)

MECHANICAL (%)

TOTAL (%)

Engineering Code By Discipline

ARCHITECTURAL %

ELECTRICAL %

MECHANICAL %

STRUCTURAL %

TOTAL %

Material Code Status

72%

68%

48%

32%

10%

10%

Planned Material

Submitted Material

Approved Material

Remaining Material

Revise & Resubmit ...

Under Review Mater...

Engineering Code Status

100%

51%

49%

37%

9%

5%

Planned Drawi...

Submitted Drawings

Not Submitted Dra...

Approved Drawings

Revise & Resubmit ...

Under Review Drawi...

DA-EN-MUP-CL...

Enlarged Drawings Clinic - GF ID1621B Approval

50%

100%

In Progress

16-Mar-25

12-Aug-25

DA-EN-MUP-C...

Enlarged Drawings Corridor - In front of Patient Room Appr...

100%

100%

Completed

10-Mar-25

19-Apr-25

DA-EN-MUP-ER...

Enlarged Drawings ER Treatment GF-03 - ER-GR-46 - ID162...

50%

100%

In Progress

16-Mar-25

12-Aug-25

DA-EN-MUP-IC...

Enlarged Drawings ICU - L02 MEQ 406 Approval

50%

100%

In Progress

16-Mar-25

12-Aug-25

DA-EN-MUP-LD...

Enlarged Drawings LDR - ID1630B-L03 Approval

50%

100%

In Progress

16-Mar-25

12-Aug-25

DA-EN-MUP-N...

Enlarged Drawings Nurse Station - L04 ID1634A & B Approv...

50%

100%

In Progress

15-Mar-25

12-Aug-25

DA-EN-MUP-PA...

Enlarged Drawings Patient Room with Toilet - L04 - 057 and ...

100%

100%

Completed

04-Sep-24

10-Jun-25

DA-EN-MUP-PH...

Enlarged Drawings LDR - ID1630B-L03 Approval

100%

100%

Completed

16-Mar-25

19-Apr-25

DA-EN-MUP-R...

Enlarged Drawings Renal Dialysis Treatment L01-011-ID1625...

50%

100%

In Progress

16-Mar-25

12-Aug-25

DA-EN-MUP-W...

Enlarged Drawings Waiting L03 - ID1631B Approval

50%

100%

In Progress

16-Mar-25

12-Aug-25

1.C...

5....

6.C...

7.P...

Dup...

11.

8.E...

9.P...

12.

Cur...

Cur...

Ove...

Cur...

Par...

AR...

Mec...

Dat...

Dat...

Dat...

Dat...

Dat...

Dat...

Dat...

Dat...

SR. PLANNING

Project Zones

All Zones

Z1

MB

1st

2nd

3rd

4th

Concrete Element

- ☐ Select all
- ☐ Column
- ☐ R Wall
- ☐ Raft
- ☐ Ramp
- ☐ S.Wall
- ☐ Screed
- ☐ Slab
- ☐ Tank Wall

Over All Progress

BudgetedTotalCost	690.00M
Data Date	31-Jul-25
Earned Value Cost	251.15M
Planned Value Cost	244.86M
BL Project Start	15-Jul-24
BL Project Finish	17-Jul-24
Earliest Actual Start	15-Jul-24
Forecast Completion Date	15-Sep-26
Elapsed Days DD	281


Concrete Quantities By Elements

	Budget Qty	Actual Qty	Performance %
	88,996.17	83,269.00	93.56%


Concrete Quantities By Floors

FLOOR	Budget Qty	Actual Qty	Actual_%
B1	1,333.00	1,333.00	100%
B1	1,730.00	1,730.00	100%
B2	272.00	272.00	100%
B2	445.60	446.00	100%
B2	989.00	989.00	100%
B2	1,379.00	1,379.00	100%
GF	938.00	938.00	100%
B1	421.00	421.00	100%
2nd	3,850.01	3,850.00	100%
FL	27,220.00	27,219.00	100%
B2	12,749.99	12,749.00	100%
B1	13,464.00	13,463.00	100%
2nd	369.85	369.00	100%
4th	200.47	200.00	100%
4th	139.44	139.00	100%
B1	264.97	264.00	100%

Raft Foundation Status

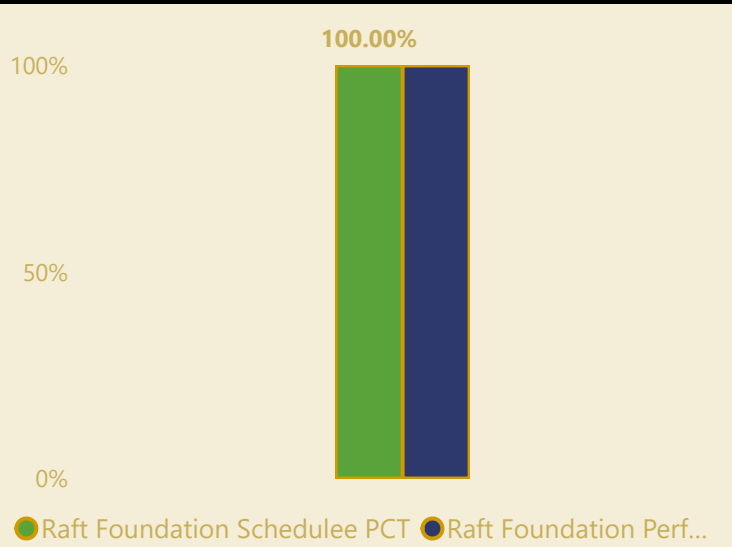


Columns Status

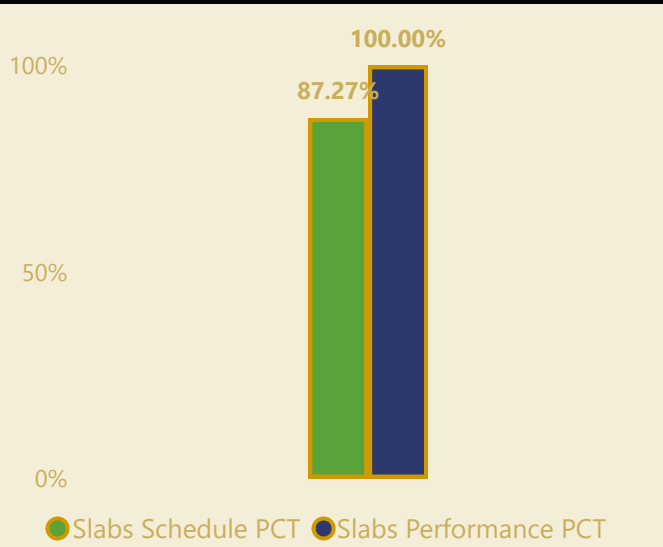


Earned Value & Sch. Value

Measures: ● Sum of (*)Earned Value

Walls Status

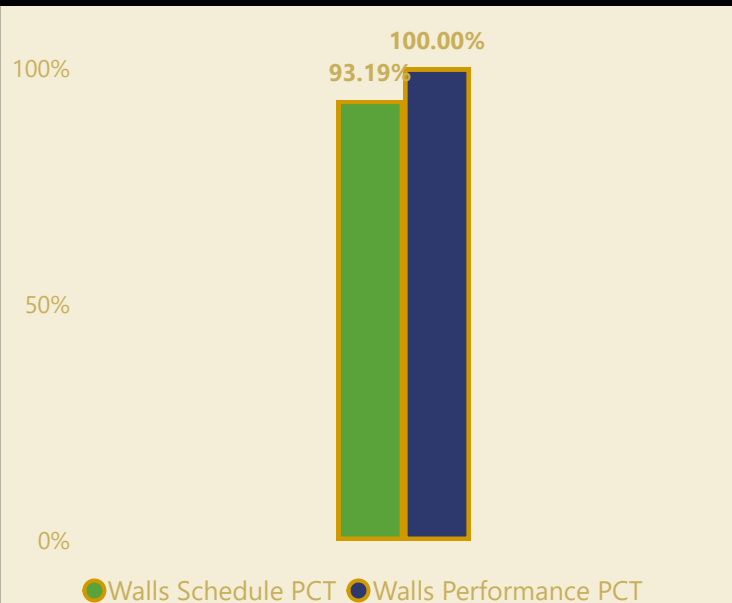

Slabs Status

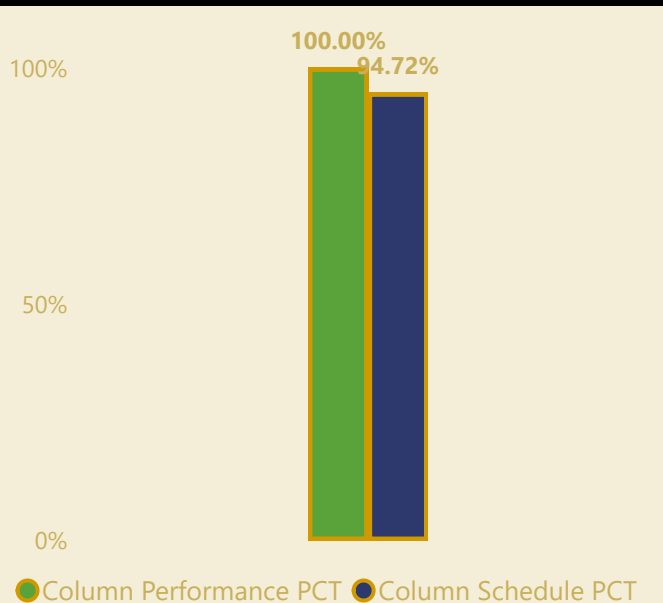

Activity Status

- ☐ Select all
- ☐ Completed
- ☐ In Progress
- ☐ Not Started

Zone

- ☐ Select all
- ☐ Z1
- ☐ Z2
- ☐ Z3
- ☐ Z4

Discipline

- ☐ Select all
- ☐ (Blank)
- ☐ all
- ☐ Arch
- ☐ Civil

2 Weeks Ahead

- ☐ Select all
- ☐ Upcoming

Progress WBS Trend

Activity ID	WBS Name	Sch. %	Perf. %	Planned Start	Planned Finish	Forecast Finish	SPI
DA-C-CUP-B02-A-28-30	Access Control	100%	0%	29-Nov-25	15-Dec-25	15-Dec-25	
DA-C-M1-B01-C-09-130	Acoustical Metal Pan Ceiling (Aluminum Tiles)	90%	0%	22-Sep-25	15-Oct-25	15-Oct-25	
DA-C-M1-B01-06-160	Aluminum Windows	90%	0%	21-Aug-25	25-Sep-25	25-Sep-25	
DA-C-M1-GR-06-160	Aluminum Windows	57%	0%	08-Oct-25	11-Nov-25	11-Nov-25	
DA-C-PA-B01-S-2590	BackFilling Around Retaining Wall Of First Basement	100%	80%	18-May-25	24-Jun-25	12-Aug-25	
DA-C-CUP-B01-04-010	Block Works	100%	90%	14-Jun-25	26-Jun-25	14-Aug-25	
DA-C-CUP-GR-04-010	Block Works	100%	85%	14-Jun-25	06-Jul-25	24-Aug-25	
DA-C-M1-L02-04-030	Block Works	100%	85%	10-Aug-25	23-Aug-25	14-Aug-25	
DA-C-CUP-GR-P-26-050	Cabling (LV),MV	50%	0%	27-Aug-25	14-Sep-25	14-Sep-25	
DA-C-M1-B02-P-26-050	Cabling (LV),MV	100%	90%	03-Aug-25	06-Sep-25	20-Sep-25	
DA-C-M1-B02-P-26-060	Cabling (LV),MV	93%	0%	21-Sep-25	26-Oct-25	26-Oct-25	
DA-C-M1-L01-P-26-050	Cabling (LV),MV	100%	0%	27-Aug-25	18-Sep-25	18-Sep-25	
DA-C-PA-B02-P-26-050	Cabling (LV),MV	100%	0%	10-Aug-25	13-Sep-25	13-Sep-25	
DA-C-PA-B02-P-26-060	Cabling (LV),MV	97%	0%	14-Sep-25	19-Oct-25	19-Oct-25	

Progress Activity Trend

Activity ID	Activity Name	Sch. %	Perf. %	Planned Start	Planned Finish	Forecast Finish	SPI
DA-C-M1-L02-07-070	Moisture And Thermal -Wet Areas Insualtion	7%	0%	30-Oct-25	03-Dec-25	03-Dec-25	
DA-C-M1-L01-C-09-020	2nd Fix - Ceiling Painting 1st coat paint Installtion	10%	0%	30-Sep-25	11-Oct-25	11-Oct-25	
DA-C-M1-L02-S-21-010	1st Fix - Installtion Of Ductwork & Hungers	10%	0%	18-Aug-25	09-Sep-25	09-Sep-25	
DA-C-M1-GR-W-09-250	2nd Fix - 1st layer Epoxy	13%	0%	21-Oct-25	24-Nov-25	24-Nov-25	
DA-CUP-B01-S-21-020	2nd Fix - Insulation Installation & Chilled Installation	27%	0%	13-Aug-25	16-Sep-25	16-Sep-25	
DA-C-CUP-GR-D-23-010	1st Fix - Installtion Of Ductwork & Hungers	27%	0%	01-Oct-25	04-Nov-25	04-Nov-25	
DA-C-M1-GR-10-070	Planters Waterproofing Installation	30%	0%	25-Sep-25	18-Oct-25	18-Oct-25	
DA-C-M1-RF-07-80	250 Micron Vapor Barrier Polyurethane Sheets	30%	0%	02-Aug-25	12-Aug-25	12-Aug-25	
DA-C-LAD-EIE-26-0310	Installation of fuel lines, including pipes and fittings, connecting the fuel source to the equipment.	32%	0%	24-Sep-25	22-Oct-25	22-Oct-25	
DA-C-M1-GR-F-09-080	1st Fix - Prperation & Putty	35%	0%	11-Oct-25	02-Nov-25	02-Nov-25	
DA-CUP-B01-D-23-020	2nd Fix - Insulation Installation & Chilled Installation	40%	0%	18-Oct-25	09-Nov-25	09-Nov-25	
DA-C-M1-GR-C-09-070	1st Fix - Setting up the framework and base for the gypsum boards	43%	20%	22-Sep-25	27-Oct-25	08-Oct-25	
DA-C-CUP-GR-S-21-010	1st Fix - Installtion Of Ductwork & Hungers	44%	0%	25-Aug-25	14-Sep-25	14-Sep-25	
DA-C-CUP-GR-P-26-050	1st Fix - Pipes & Boxes Installation	50%	0%	27-Aug-25	14-Sep-25	14-Sep-25	
DA-C-M1-B01-W-09-170	2nd Fix - Framing installation	53%	0%	17-Nov-25	21-Dec-25	21-Dec-25	
DA-C-M1-GR-06-160	1st Fix - Window Frame Installation	57%	0%	08-Oct-25	11-Nov-25	11-Nov-25	
DA-C-M1-FIV-07-60	External Facade - Thermal Insulation Installation	60%	0%	24-Aug-25	15-Sep-25	15-Sep-25	

Work Type

Engineering Progress Trend

Activity Status

Activity Status

Activity ID	Activity Name	(*)WBS Name	(*)Schedule % Complete(%)	(*)Performance % Complete(%)	SPI	(*)Early Start	(*)Early Finish	(*)Total Float(d)
DA-EN-CV-SU-400	Steel Structure Canopy_Shop Drawings Submittal	Concrete Work	100.00	0.00	-1	02-Aug-25	09-Aug-25	-106.00
DA-EN-CV-SU-500	Site Structural Columns_Shop Drawings Submittal	Concrete Work	100.00	0.00	-1	02-Aug-25	09-Aug-25	-106.00
DA-EN-CV-SU-510	Site Structural Foundation_Shop Drawings Submittal	Concrete Work	100.00	0.00	-1	10-Aug-25	13-Aug-25	-106.00
DA-EN-CV-SU-520	Site Landscape Structural Sections_Shop Drawings Submittal	Concrete Work	100.00	0.00	-1	10-Aug-25	13-Aug-25	-106.00
DA-EN-CV-AP-510	Site Structural Foundation_Shop Drawings Approval	Concrete Work	100.00	0.00	-1	14-Aug-25	21-Aug-25	-106.00
DA-EN-CV-AP-520	Site Landscape Structural Sections_Shop Drawings Approval	Concrete Work	100.00	0.00	-1	14-Aug-25	21-Aug-25	-106.00
DA-EN-CV-AP-400	Steel Structure Canopy_Shop Drawings Approval	Concrete Work	100.00	0.00	-1	10-Aug-25	17-Aug-25	-102.00
DA-EN-CV-AP-500	Site Structural Columns_Shop Drawings_Shop Drawings Appro...	Concrete Work	100.00	0.00	-1	10-Aug-25	17-Aug-25	-102.00
DA-C-M1-RF-07-100	Geotextile Filter Fabric	Roof Water Proofing	0.00	0.00	1	20-Nov-25	01-Dec-25	-48.00
DA-C-M1-RF-07-110	50Mm Min. Thickness Foam Concrete	Roof Water Proofing	0.00	0.00	1	26-Nov-25	07-Dec-25	-48.00
DA-C-M1-RF-07-120	4Mm Two Layer Water Proofing	Roof Water Proofing	0.00	0.00	1	08-Dec-25	18-Dec-25	-48.00
DA-C-M1-RF-07-140	Cast In Place Stamped Concrete	Roof Water Proofing	0.00	0.00	1	05-Mar-26	16-Mar-26	-48.00
DA-C-M1-1RF-F-07-030	Gravel Wearing Coarse Installation	Gravel Wearing Coarse	0.00	0.00	1	05-Mar-26	22-Mar-26	-41.00
DA-PR-NL-CV-MD-200	WaterpROofing Primer_Material Delivery	Thermal	100.00	80.00	-1	02-Aug-25	04-Aug-25	-36.00
DA-PR-NL-CV-MD-180	WaterpROofing Membrane_Material Delivery	Thermal	100.00	80.00	-1	02-Aug-25	06-Aug-25	-36.00
DA-PR-NL-CV-MD-190	Fluid Membrane_Material Delivery	Thermal	100.00	80.00	-1	02-Aug-25	06-Aug-25	-36.00
DA-PR-NL-CV-SU-010	Asphalt Works_Material Submission	Exterior Improvements	100.00	0.00	-1	01-Nov-25	08-Nov-25	-30.00
DA-PR-NL-CV-AP-010	Asphalt Works_Material Approval	Exterior Improvements	100.00	0.00	-1	09-Nov-25	25-Nov-25	-30.00
DA-PR-NL-CV-PO-010	Asphalt Works_Purchase Order	Exterior Improvements	100.00	0.00	-1	26-Nov-25	13-Dec-25	-30.00
DA-PR-NL-CV-MD-010	Asphalt Works_Material Delivery	Exterior Improvements	38.89	0.00	-1	14-Dec-25	05-Mar-26	-30.00
DA-C-LND-RD-32-011	Base Layer Installation, Lay down a gravel or aggregate base	Construction	0.00	0.00	1	07-Mar-26	04-Apr-26	-30.00
DA-C-LND-RD-32-012	Pavement, Pour asphalt or lay concrete for the road surface	Construction	0.00	0.00	1	07-Mar-26	07-Apr-26	-30.00
DA-C-M1-B02-07-020	2nd Fix - Sealing	Interior Expansion Joint	100.00	0.00	-1	06-Sep-25	20-Sep-25	-28.00
DA-C-M1-RF-07-130	Protection Board	Roof Water Proofing	0.00	0.00	1	20-Dec-25	05-Jan-26	-27.00
DA-C-LND-PL-03-010	Landscape Ventilation Shaft Concrete Covers Installation	Landscape Ventilation Shaft Concrete Covers	0.00	0.00	1	28-Jun-26	01-Aug-26	-22.00
DA-C-M1-B01-07-070	Moisture And Thermal -Wet Areas Insualtion	Moisture And Tthermal Insulation	100.00	20.00	-1	12-Aug-25	25-Aug-25	-21.00
DA-C-M1-GR-07-070	Moisture And Thermal -Wet Areas Insualtion	Moisture And Tthermal Insulation	100.00	0.00	-1	26-Aug-25	24-Sep-25	-21.00
DA-C-M1-L01-07-070	Moisture And Thermal -Wet Areas Insualtion	Moisture And Thermal Insulation	100.00	0.00	-1	25-Sep-25	29-Oct-25	-21.00
DA-C-M1-L02-07-070	Moisture And Thermal -Wet Areas Insualtion	Moisture And Thermal Insulation	6.67	0.00	-1	30-Oct-25	03-Dec-25	-21.00
DA-C-M1-RF-07-70	Cast In Place Stamped Concrete	Roof Water Proofing	0.00	0.00	1	12-Mar-26	19-Mar-26	-21.00
DA-O&M-STRU-010	Structural O & M Manuals	Structural O & M Manuals	0.00	0.00	1	12-Mar-26	06-Jul-26	-19.00
DA-SN&DS-STRU-10	Structural Snaging & De-Snagging	Structural Snagging & De-Snagging	0.00	0.00	1	12-Mar-26	18-Jul-26	-19.00
DA-PR-CV-MD-110	Control & Expansion Joints_Material Delivery	Thermal And Moisture Protection	100.00	0.00	-1	02-Aug-25	23-Aug-25	-17.00
DA-C-M1-L01-07-020	2nd Fix - Sealing	Interior Expansion Joint	100.00	0.00	-1	06-Sep-25	16-Sep-25	-16.00
DA-WAR-CIVIL-010	Structural Warranty Snagging & De Snagging	Structural Warranty Certificates	0.00	0.00	1	21-Mar-26	26-Jul-26	-16.00
DA-C-M1-2RF-F-07-030	Gravel Wearing Coarse Installation	Gravel Wearing Coarse	0.00	0.00	1	12-Mar-26	23-Mar-26	-15.00
DA-C-M1-GR-07-020	2nd Fix - Sealing	Interior Expansion Joint	100.00	0.00	-1	06-Sep-25	17-Sep-25	-12.00

Activity Status

Procurement Progress Trend

Select all

(Blank)

all

Arch

Civil

Work Type

Select all

(Blank)

Ath.App

Const

Eng.AP

Eng.SU

GR

P.Miles

Activity Status

Select all

(Blank)

Completed

In Progress

1.C

5.M

6.C

7.P

Dupl

11.

8.E

12.

Cur

Cur

Ove

Cur

Part



Dat

Dat

Dat

Dat

Dat

Dat

Dat

Dat




One Month Look Ahead Flag





- ▶ ○ all ...
- ▶ ○ CUP ...
- ▶ ○ EW ...
- ▶ ● MB ...
- ▶ ○ PA ...

One Month Look Ahead WBS

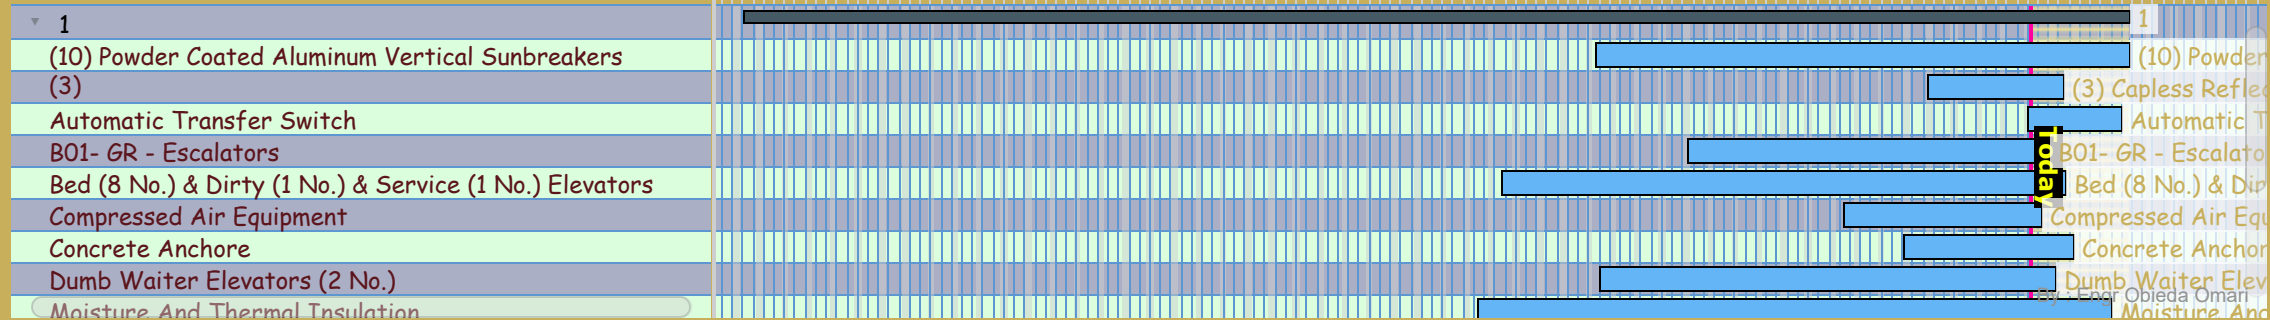

One Month Look Ahead Activities

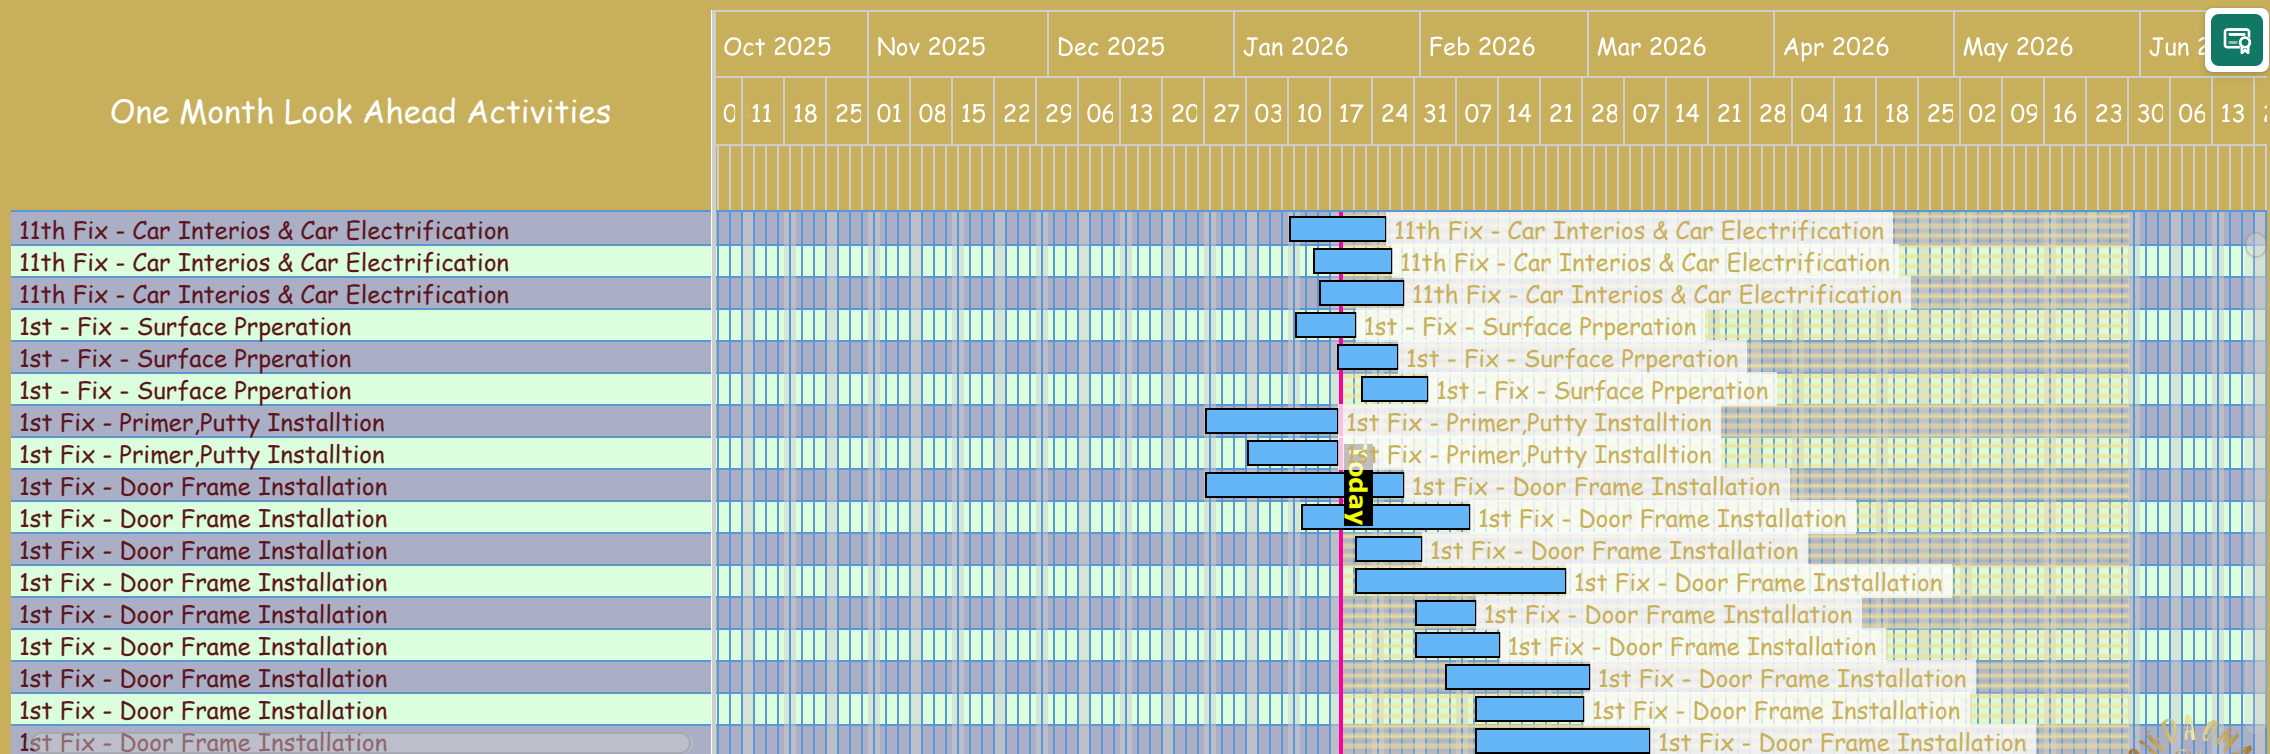

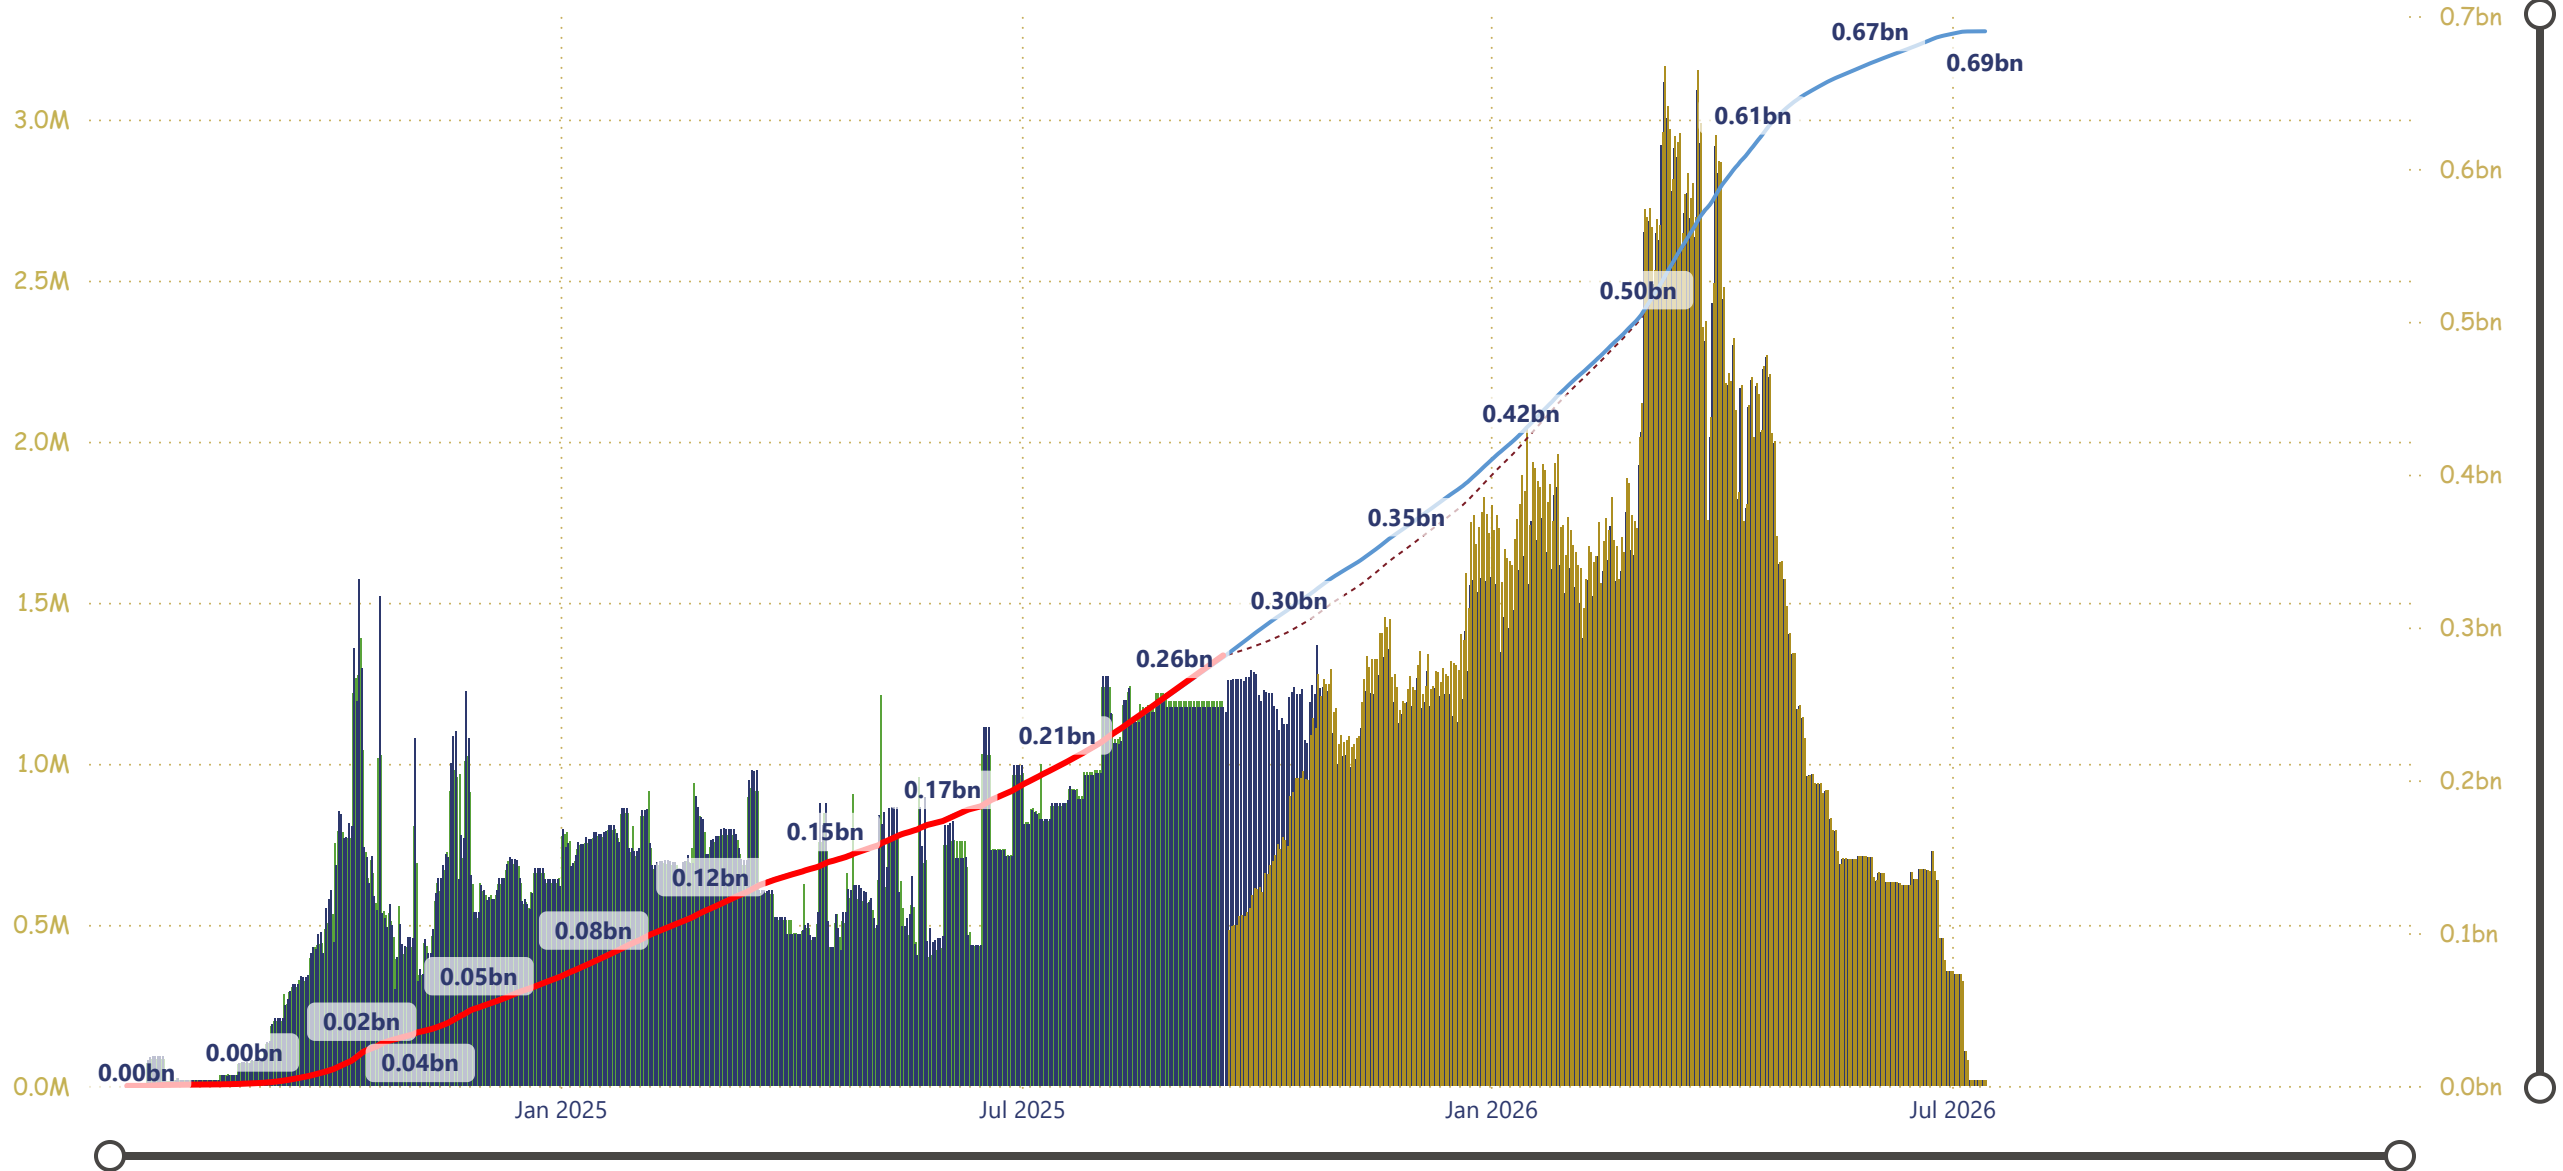

WorkDate


● Sum of Earned_Daily_OnDate
 ● Sum of Planned_Daily_OnDate
 ● Sum of Forecast_Daily_OnDate
 ● Sum of Forecast_Daily_OnDate running total in WorkDate
 ● Sum of Planned_Daily_OnDate running total in WorkDate
 ● Sum of Earned_Daily_OnDate running total...

1.09









Over All Progress

Budgeted Total Cost	52.02M
Data Date	31-Jul-25
Earned Value Cost	35.76M
Planned Value Cost	32.68M
BL Project Start	24-Aug-24
BL Project Finish	08-Sep-24
Earliest Actual Start	29-Aug-24
Forecast Completion Date	08-Jun-26
Elapsed Days DD	341
Project Duration (D)	599
Elapsed Time %	56.93%




36M 109.43%






Budgeted Total Cost

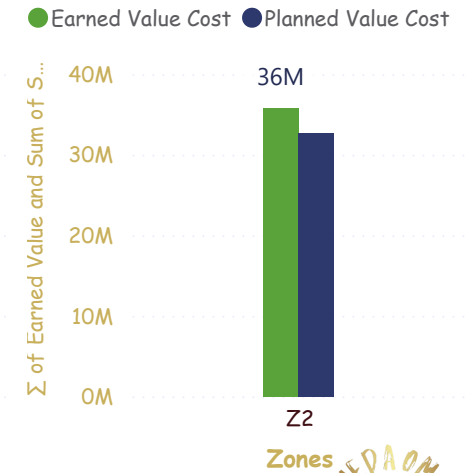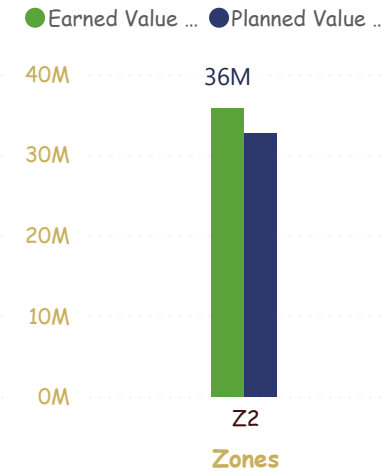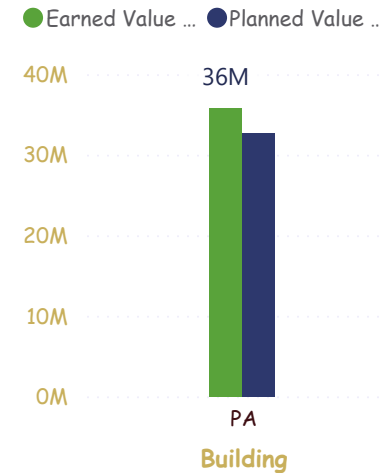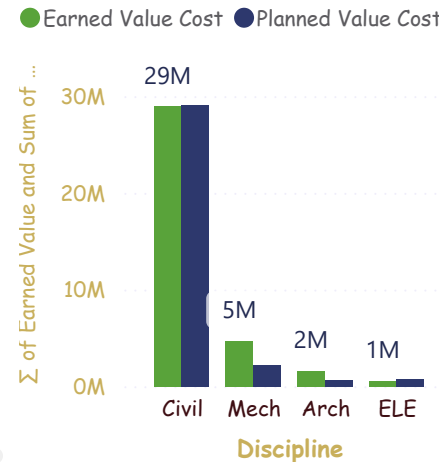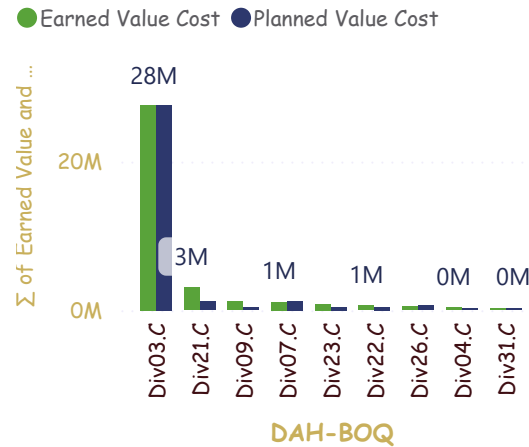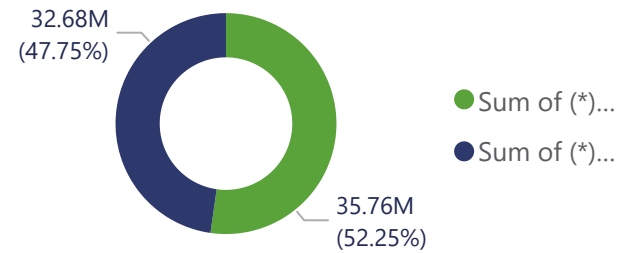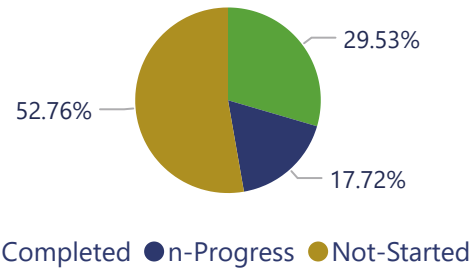


1.C ov... 5.M at... 6.C on... 7.P ro... Dupl ica... 11. Σ... 8.E ngi... 9.P ro... 12. On... C... Cur re... Ove ral... Cur re... Part ial... ARC H... Mec ha... Dat ab... Dat ab... Dat ab... Dat ab... Dat ab... Dat ab... Dat ab...

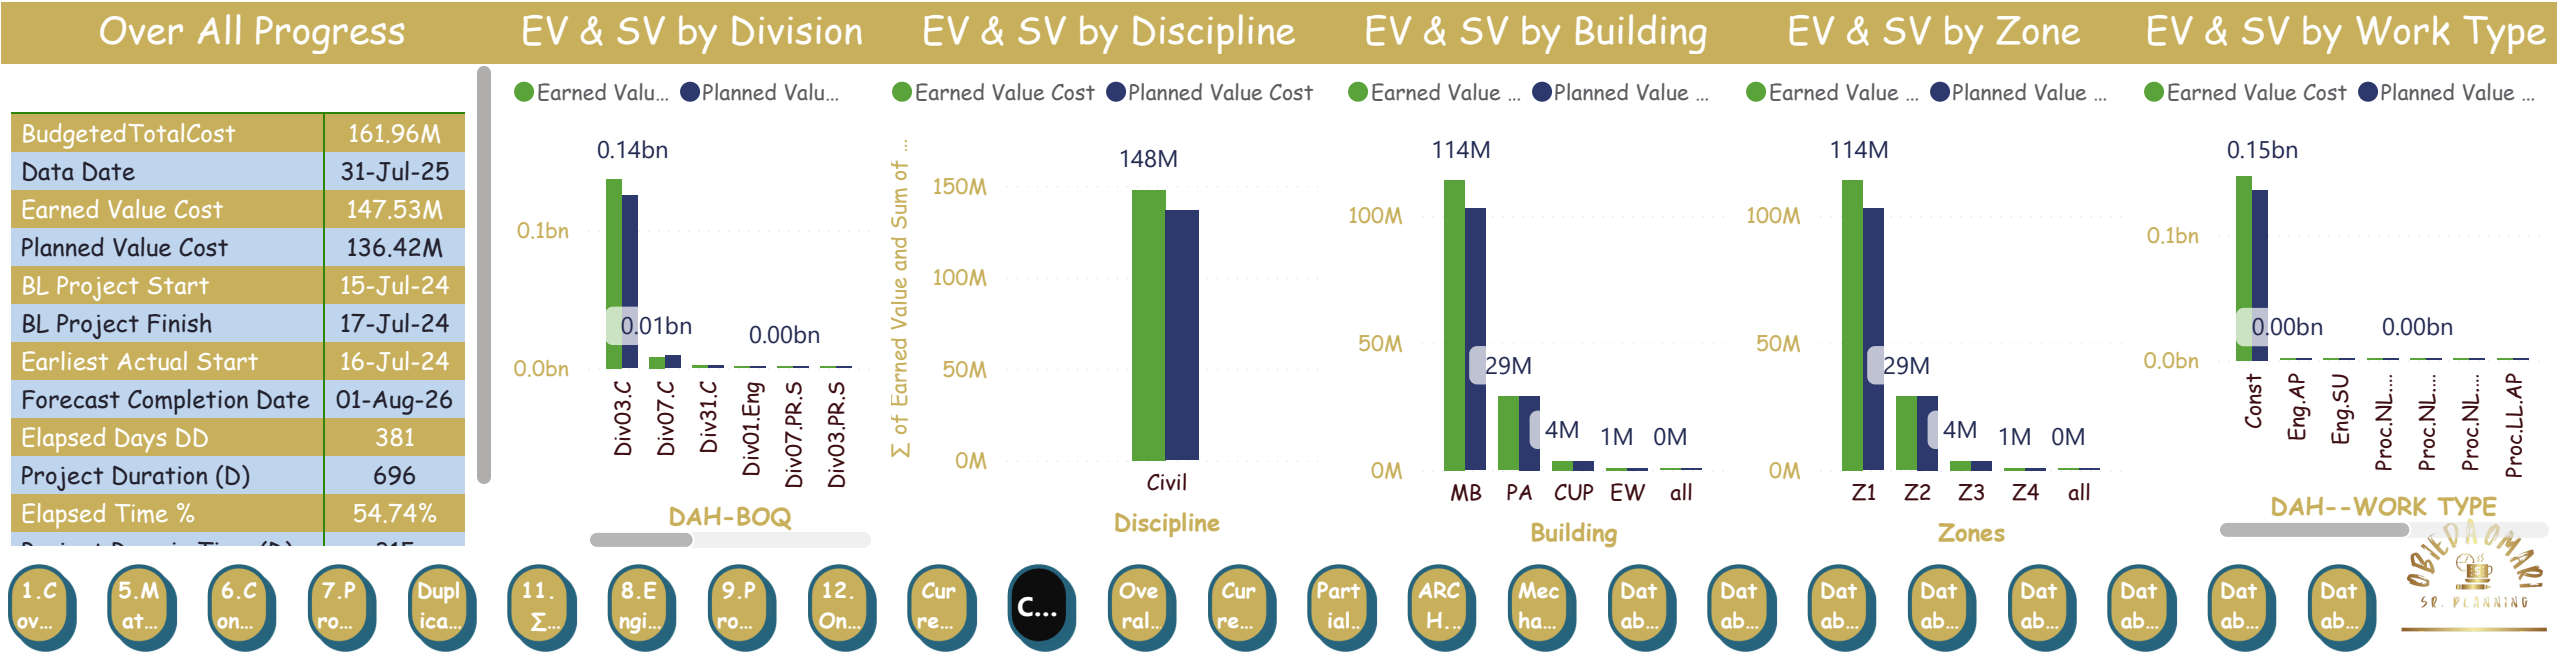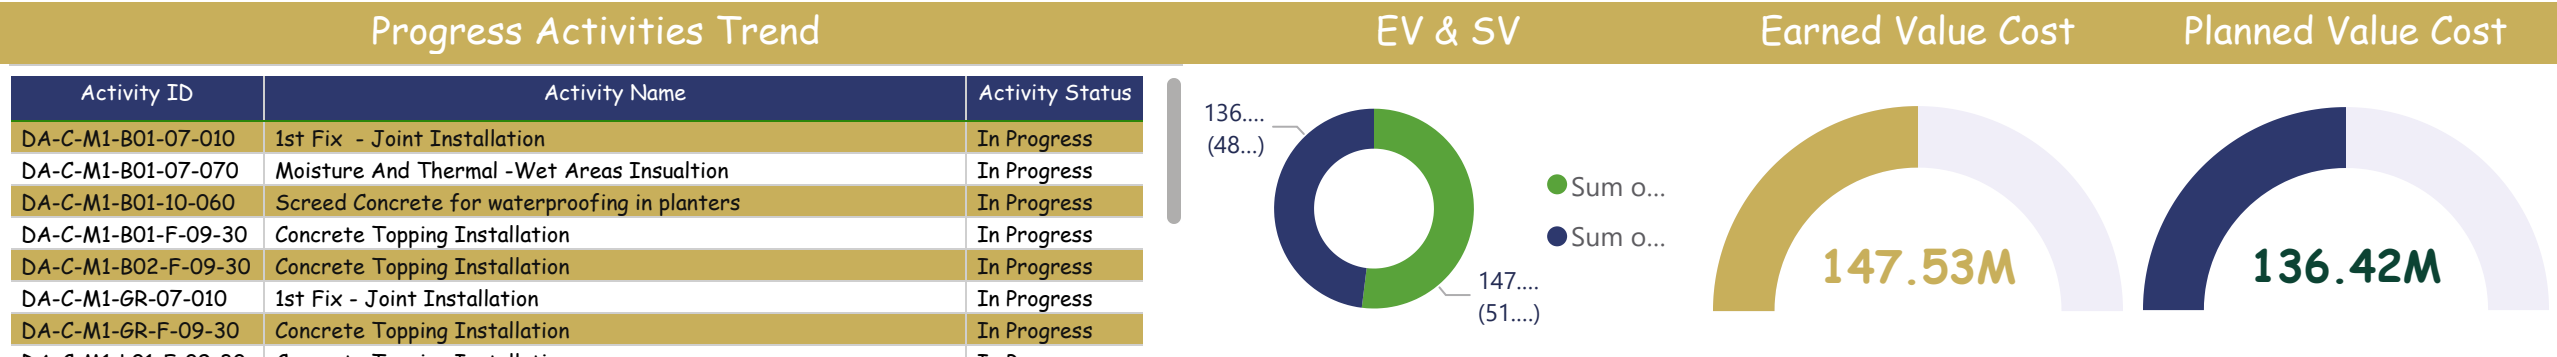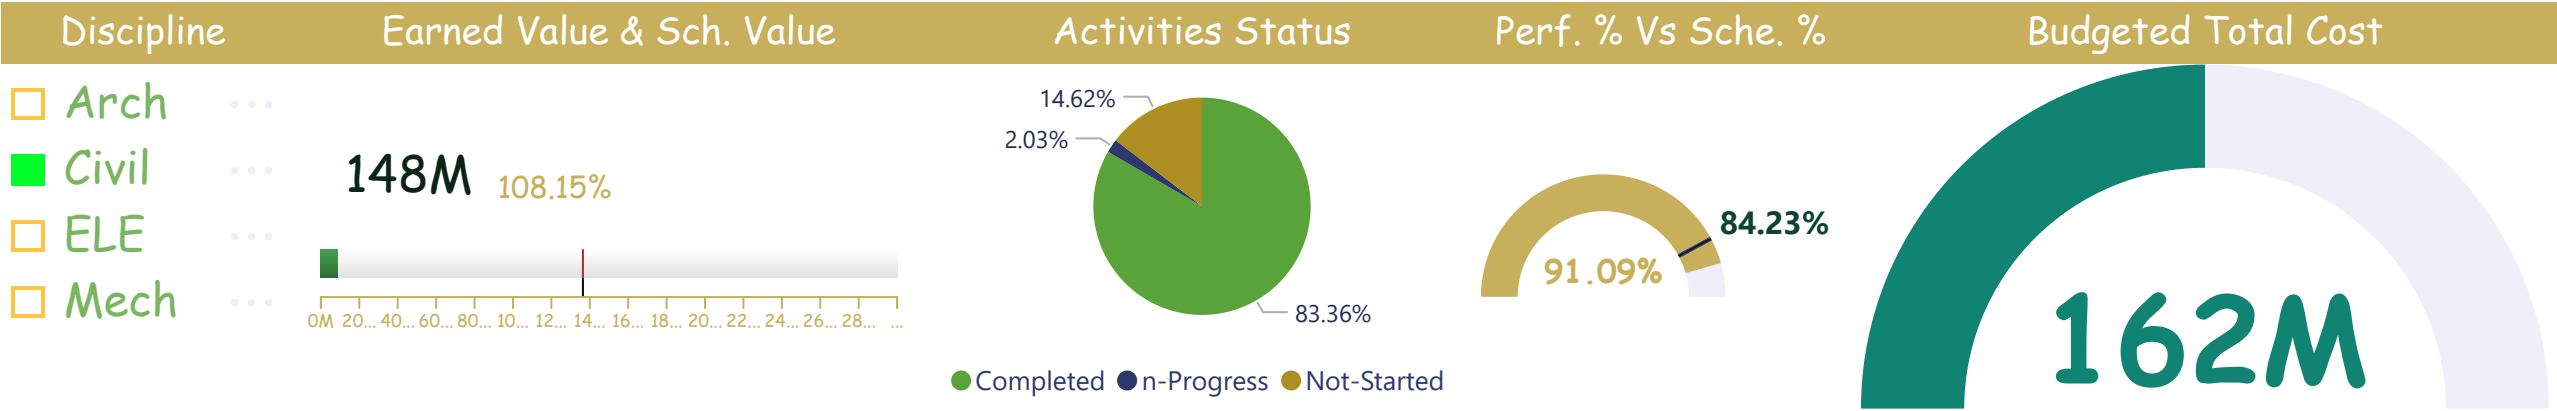

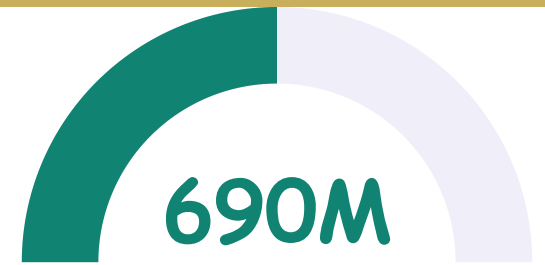


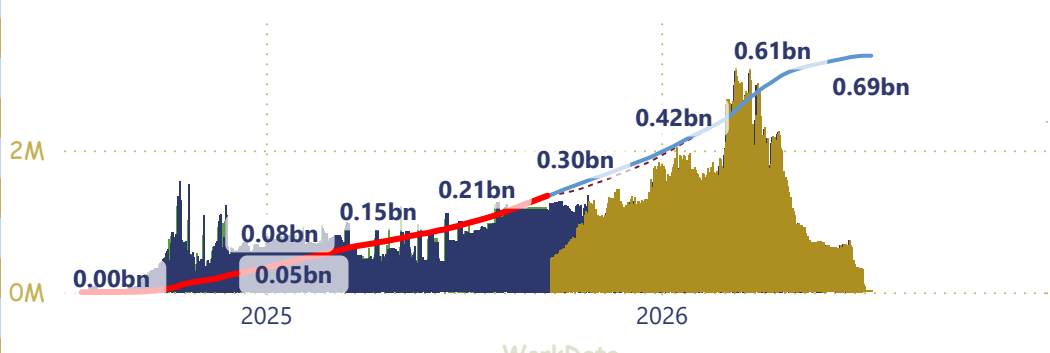		Planned, Earned, Forecast S-Curve		Earned Value Cost		Planned Value Cost	
Budgeted Total Cost	690.00M						
Planned Value Cost	244.86M						
Earned Value Cost	251.15M						
BL Project Start	15-Jul-24						
BL Project Finish	17-Jul-24						
Actual Start	15-Jul-24						
Start	15-Jul-24						
Forecast Completion Date	15-Sep-26						
Dealy / Ahead	-63						
Dealy / Ahead (Without Holiday)	-46						
SPI	1.03 						

Earned Value Cost	Planned Value Cost
$EV = PV \times \frac{Actual\ Work\ Done}{Planned\ Work}$ $EV = PV \times \frac{Actual\ Time\ Elapsed}{Planned\ Time}$	$PV = \frac{Planned\ Work}{Planned\ Time} \times Time\ Elapsed$ $PV = \frac{Planned\ Work}{Planned\ Time} \times Time\ Elapsed$

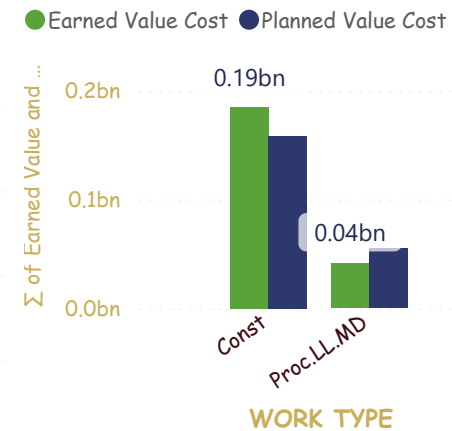

Performance % Vs Schedule %



Budgeted Total Cost	690.00M
Planned Value Cost	244.86M
Earned Value Cost	251.15M
BL Project Start	15-Jul-24
BL Project Finish	17-Jul-24
Data Date	31-Jul-25
Actual Start	15-Jul-24
Start	15-Jul-24
Forecast Completion Date	15-Sep-26
Dealy / Ahead	-63
Dealy / Ahead (Without Holiday)	-46
SPI	1.03


Project Break Down

- ▶ ● Z1
- ▶ ○ Z2
- ▶ ○ Z3

Construction Progress

Floor	Performance PCT	Schedule PCT
B2	79.00%	79.45%
B1	47.08%	44.27%
2nd	36.70%	32.38%
1st	35.91%	30.37%
GR	34.91%	29.28%
4th	26.46%	4.29%
5th	24.86%	0.99%
6th	22.31%	1.30%
3rd	19.89%	14.88%
RF	0.18%	0.69%
Total	42.69%	36.84%

Budgeted Total Cost




Earned Value Cost Planned Value Cost




Variance

0.91


EV & SV by Division

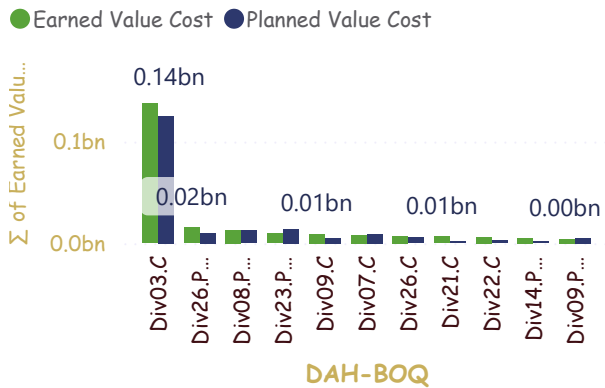


EV & SV by Discipline

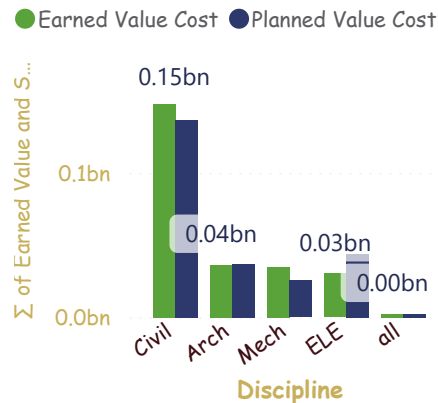


EV & SV by Building

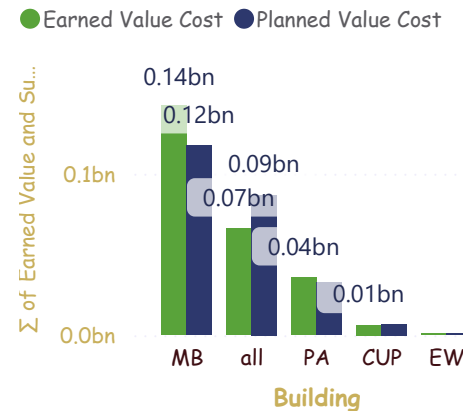

EV & SV by Zone

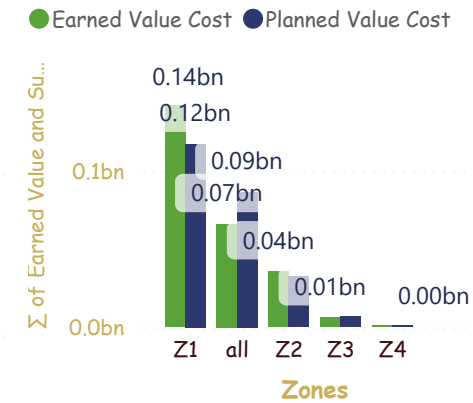

EV & SV by Work Type

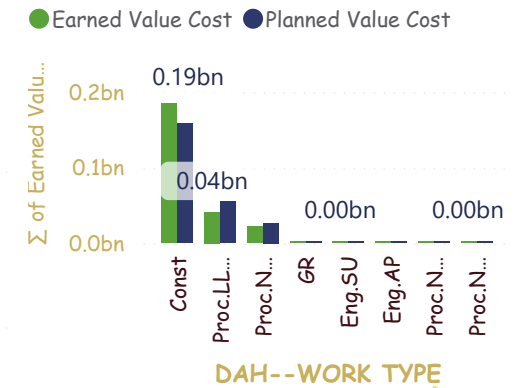

Over All Progress

Budget Total Cost	690M
Data Date	25-Sep-25
Earned Value Cost	283M
Planned Value Cost	283M
BL Project Start	15-Jul-24
BL Project Finish	14-Jul-26
Actual Start	15-Jul-24
Forecast Completion Date	06-Oct-26
Elapsed Days DD (db)	437
Project Duration (D) (db)	729
Elapsed Time % (db)	59.95%
Elapsed Time %	52.26%

Budget Cost

690M

Perf. % Vs Sch. %

40.97%

Baseline Milestone's Dates

Close

Open

Days

Months

Years

All

Task	Start	End	Days
MILESTONES	15/07/24	14/07/26	730 d
Project Start	15/07/24	15/07/24	1 d
Mobilization Completion	14/11/24	14/11/24	1 d
Main Building Concrete ...	06/08/25	06/08/25	1 d

Data.Date Deviation & SPI

Variance

0.00

S.P.I

1.00

Schedule Value

282.7M

Earned Value

282.7M

Updates Milestone's Dates

Close

Open

Days

Months

Years

All

Task	Start	End	Days
MILESTONES	15/07/24	14/07/26	730 d
Project Start	15/07/24	15/07/24	1 d
Mobilization Completion	14/11/24	14/11/24	1 d
Main Building Concrete ...	06/08/25	06/08/25	1 d
Mock-Up Rooms	25/10/25	25/10/25	1 d
Submissions And Appr...	10/12/25	10/12/25	1 d

VAR Deviation & SPI

Variance_Pa...

-1.00

SPI Partial

--

ENG

MAT

PQ

TECH

RFI

NCR

S-C

Labor

ENG Codes

Engineering Status

☐ Approved Dr...

☐ Not Submitt...

☐ Planned Dra...

☐ Revise & Res...

☐ Submitted D...

☒ Total Drawin...

☐ Under Revie...


Project SPI Trend

Earned - Planned - Variance %

Planned, Earned, Forecast S-Curve

S.P.I Partial

- Database.Cover Page
- Database.Techni...
- Database.Overall...
- Database.Current...
- Database.Current...
- Database.Current...
- Database.Current...
- Database.Partial...
- Database.Σ PV,EV,F...
- Database.Σ PV,EV,F...
- Database.Current...
- Page 4
- Page 5
- Page 6

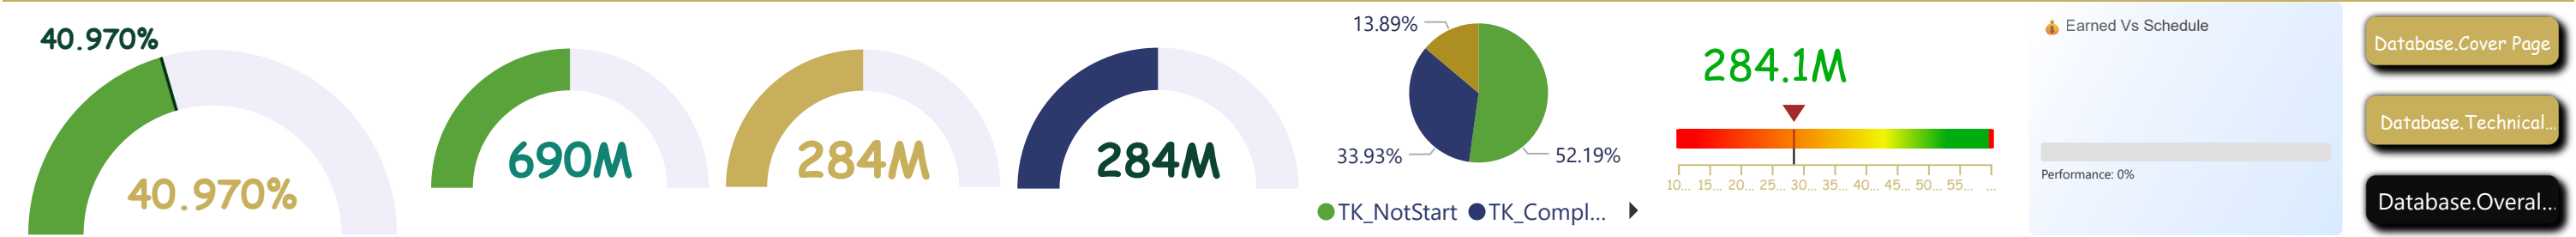

Current Progress

Project Work Breakdown Structure Indictors

Progress Activities Trend

Data Date	18-Sep-25
Budgeted Total Cost	690.00M
Earned Value Cost	282.70M
Planned Value Cost	282.70M
BL Project Start	16-Jul-24
BL Project Finish	14-Jul-26
Actual Start	15-Jul-24
Forecast Completion Date	14-Jul-26
Delay_Ahead (DB)	0
Dealy/Ahead(Without Holiday)	1
S.P.I	1.00

DISCIPLINE	BCWP	BCWS	BTC	Perf.%	Sche.%	S.P.I	Variance
all	2M	2M	3M	72%	72%	1.00	0.00
Arch	46M	46M	199M	23%	23%	1.00	0.00
Civil	148M	148M	162M	91%	91%	1.00	0.00
ELE	40M	40M	170M	24%	24%	1.00	0.00
Mech	47M	47M	156M	30%	30%	1.00	0.00
Total	283M	283M	690M	41%	41%	1.00	0.00

Activity ID	Activity Name	Activity Status
DA-C-PA-B02-W-09-3...	1st Fix - Primer,Putty Installtion	TK_Active
DA-CUP-B02-W-09-320	1st Fix - Primer,Putty Installtion	TK_Active
DA-C-M1-B02-P-14-010	1st Fix - Compressor Installation, Piping Installation, Air Treatment Com...	TK_Active
DA-C-M1-GR-P-14-010	1st Fix - Compressor Installation, Piping Installation, Air Treatment Com...	TK_Active
DA-C-M1-L01-P-14-010	1st Fix - Compressor Installation, Piping Installation, Air Treatment Com...	TK_Active
DA-C-M1-L02-P-14-010	1st Fix - Compressor Installation, Piping Installation, Air Treatment Com...	TK_Active
DA-C-M1-L04-P-14-010	1st Fix - Compressor Installation, Piping Installation, Air Treatment Com...	TK_Active
DA-C-M1-L05-P-14-010	1st Fix - Compressor Installation, Piping Installation, Air Treatment Com...	TK_Active
DA-C-M1-L06-P-14-010	1st Fix - Compressor Installation, Piping Installation, Air Treatment Com...	TK_Active
DA-C-M1-B01-W-09-110	1st Fix - Install Framework, Install Track and Stud System, Floor and C...	TK_Active
DA-C-M1-L01-W-09-110	1st Fix - Install Framework, Install Track and Stud System, Floor and C...	TK_Active

EV & SV by Discipline


EV & SV by Building

EV & SV by Zone

EV & SV by Work Type


S-Curve (Monthly Distribution)



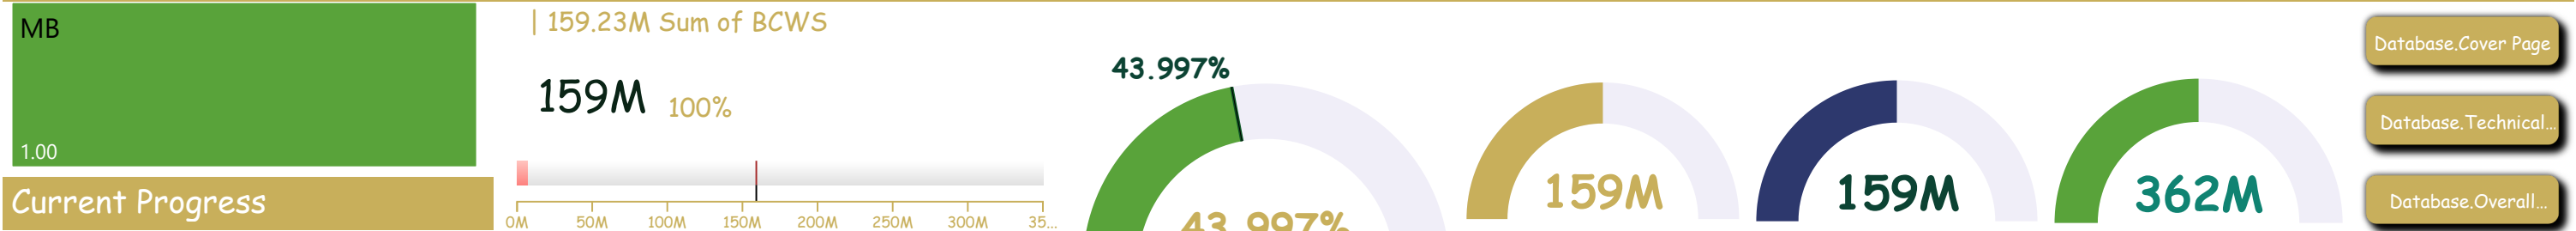

Current Progress

Data Date	18-Sep-25
Budgeted Total Cost	361.92M
Earned Value Cost	159.23M
Planned Value Cost	159.23M
BL Project Start	25-Jul-24
BL Project Finish	06-Jul-26
Actual Start	15-Jul-24
Forecast Completion Date	11-Apr-26
Delay_Ahead (DB)	-63
Dealy/Ahead(Without Holiday)	-45
S.P.I	1.00
Elapsed_Days_DB	420

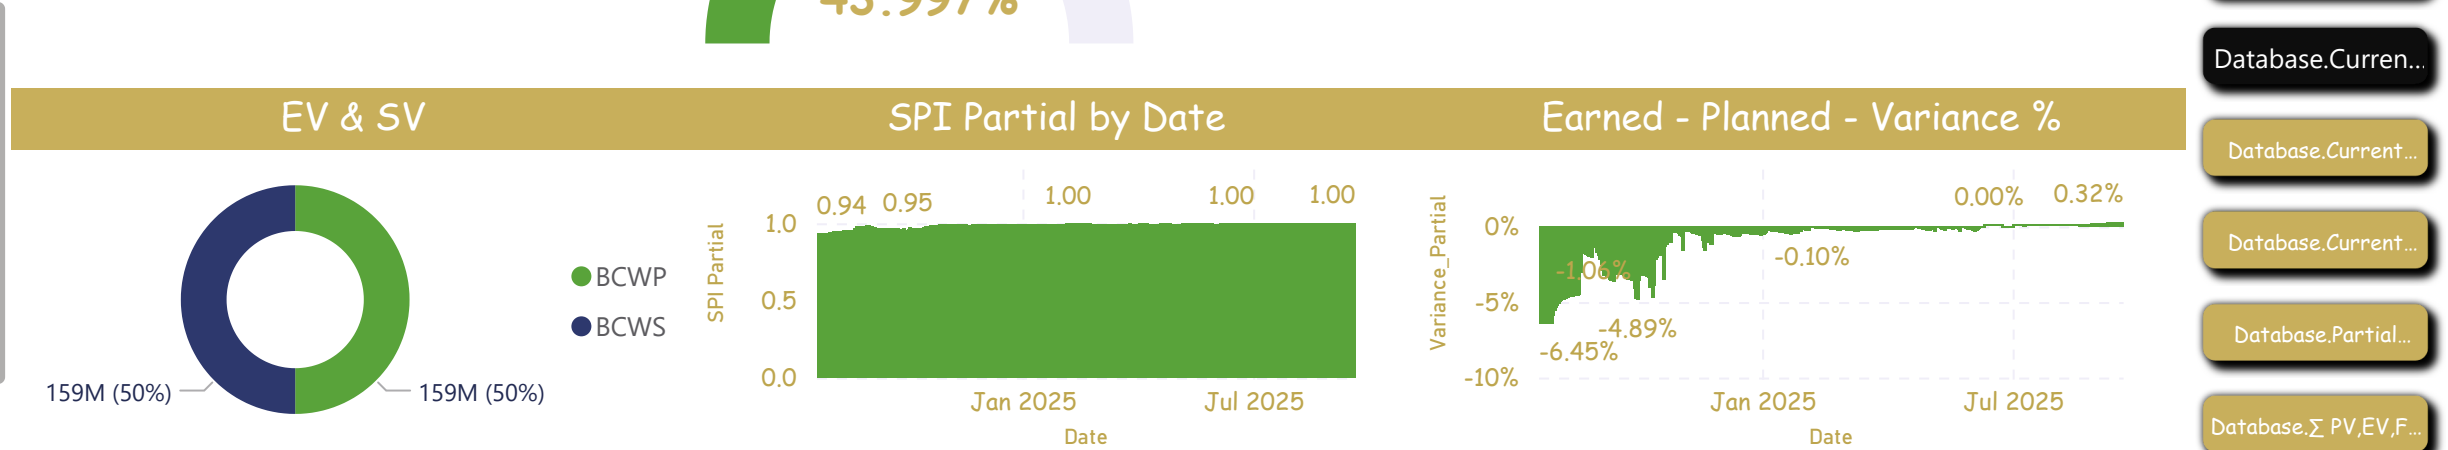

ZONE

EV & SV by Division


EV & SV by Discipline

EV & SV by Building

EV & SV by Zone

EV & SV by Work Type

Activities Status

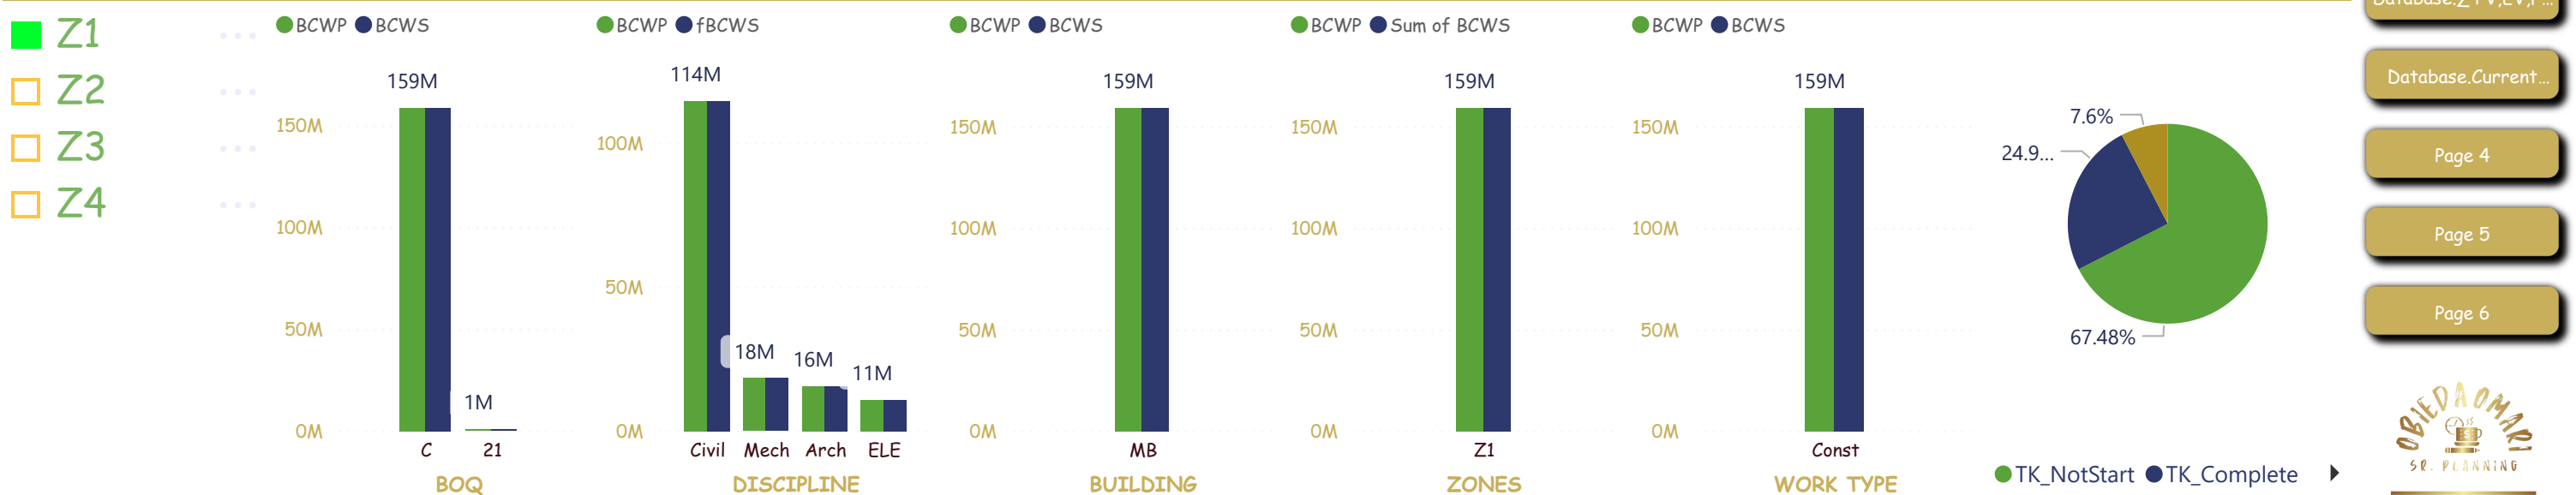

Building

WBS: CUP

► ● CUP

▶ ○ MB

▶ ○ PA

Discipline

WBS: Arch

 Arch

○ Civil

○ ELE

○ Mech

Construction Progress


Floor

Performance PCT


Schedule PCT

B2	17.90%	86.09%
B1	8.21%	18.29%
GR	2.21%	2.60%
1st	6.42%	
RF		

Planned, Earned, Forecast S-Curve

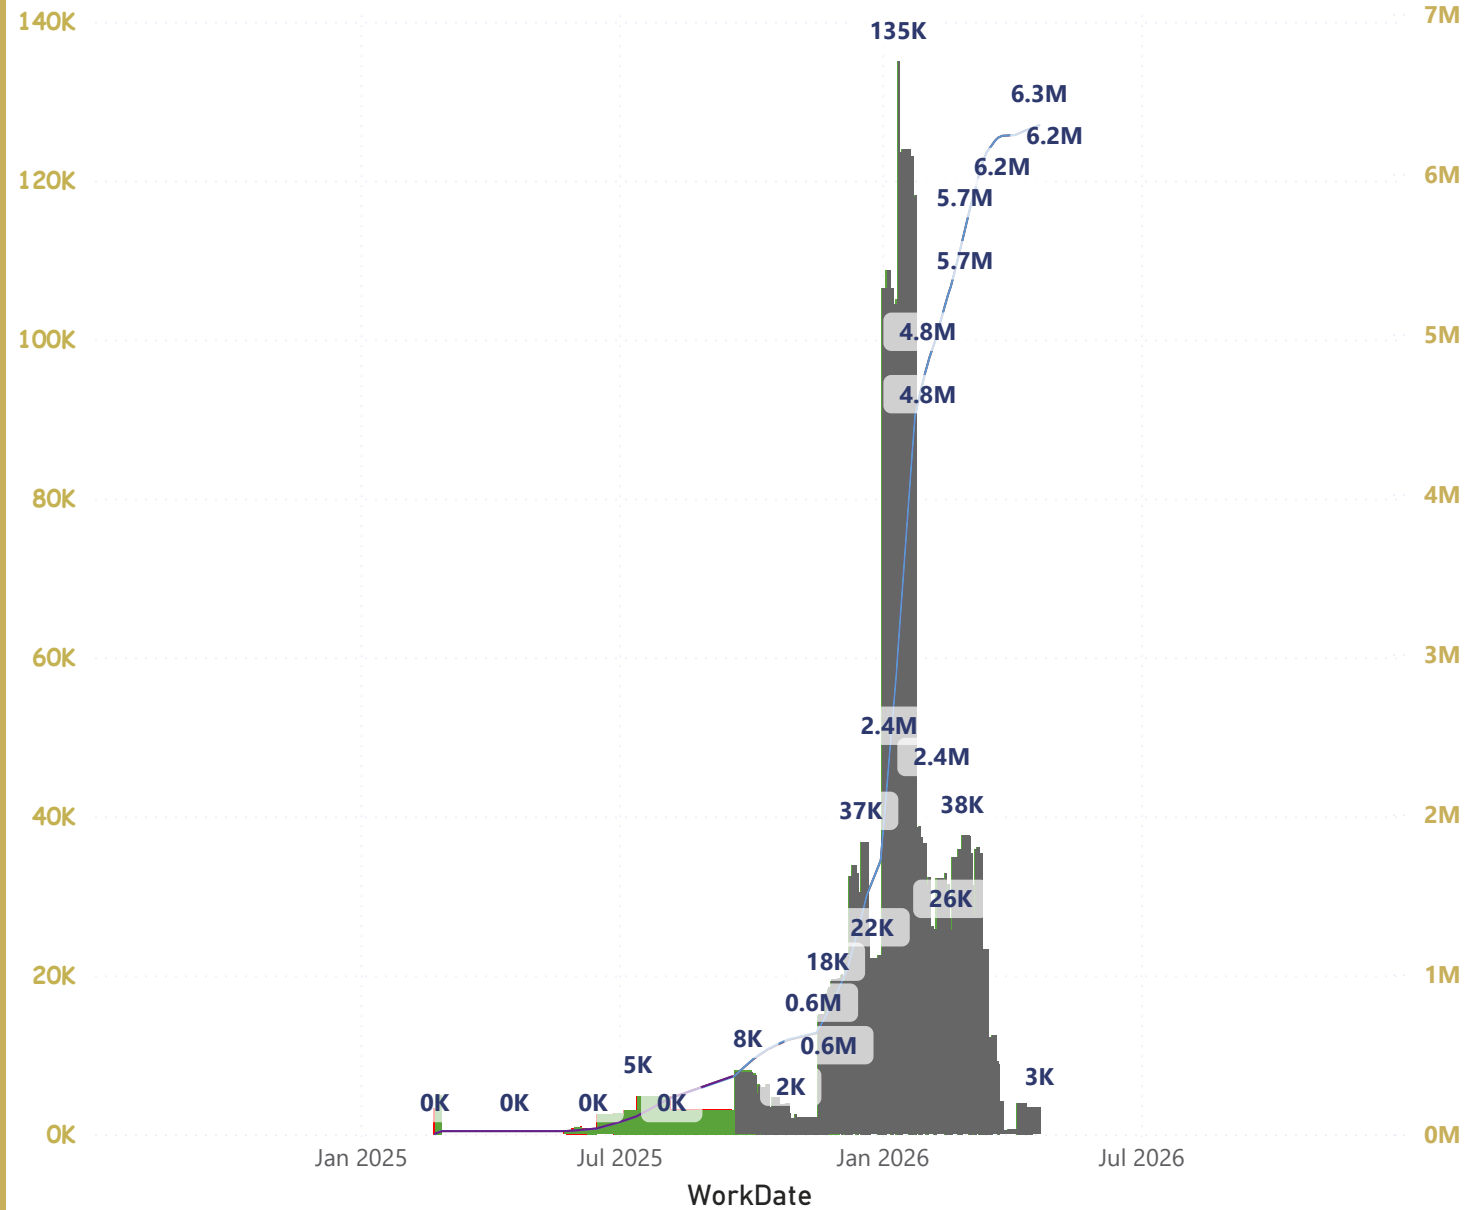

● Sum of Earned_Daily_On... ● Sum of Planned_Daily_... ● Sum of Forecast_Dail... ● Sum of Forecast_... ● Sum of Planned_... ● Sum of Earned_...

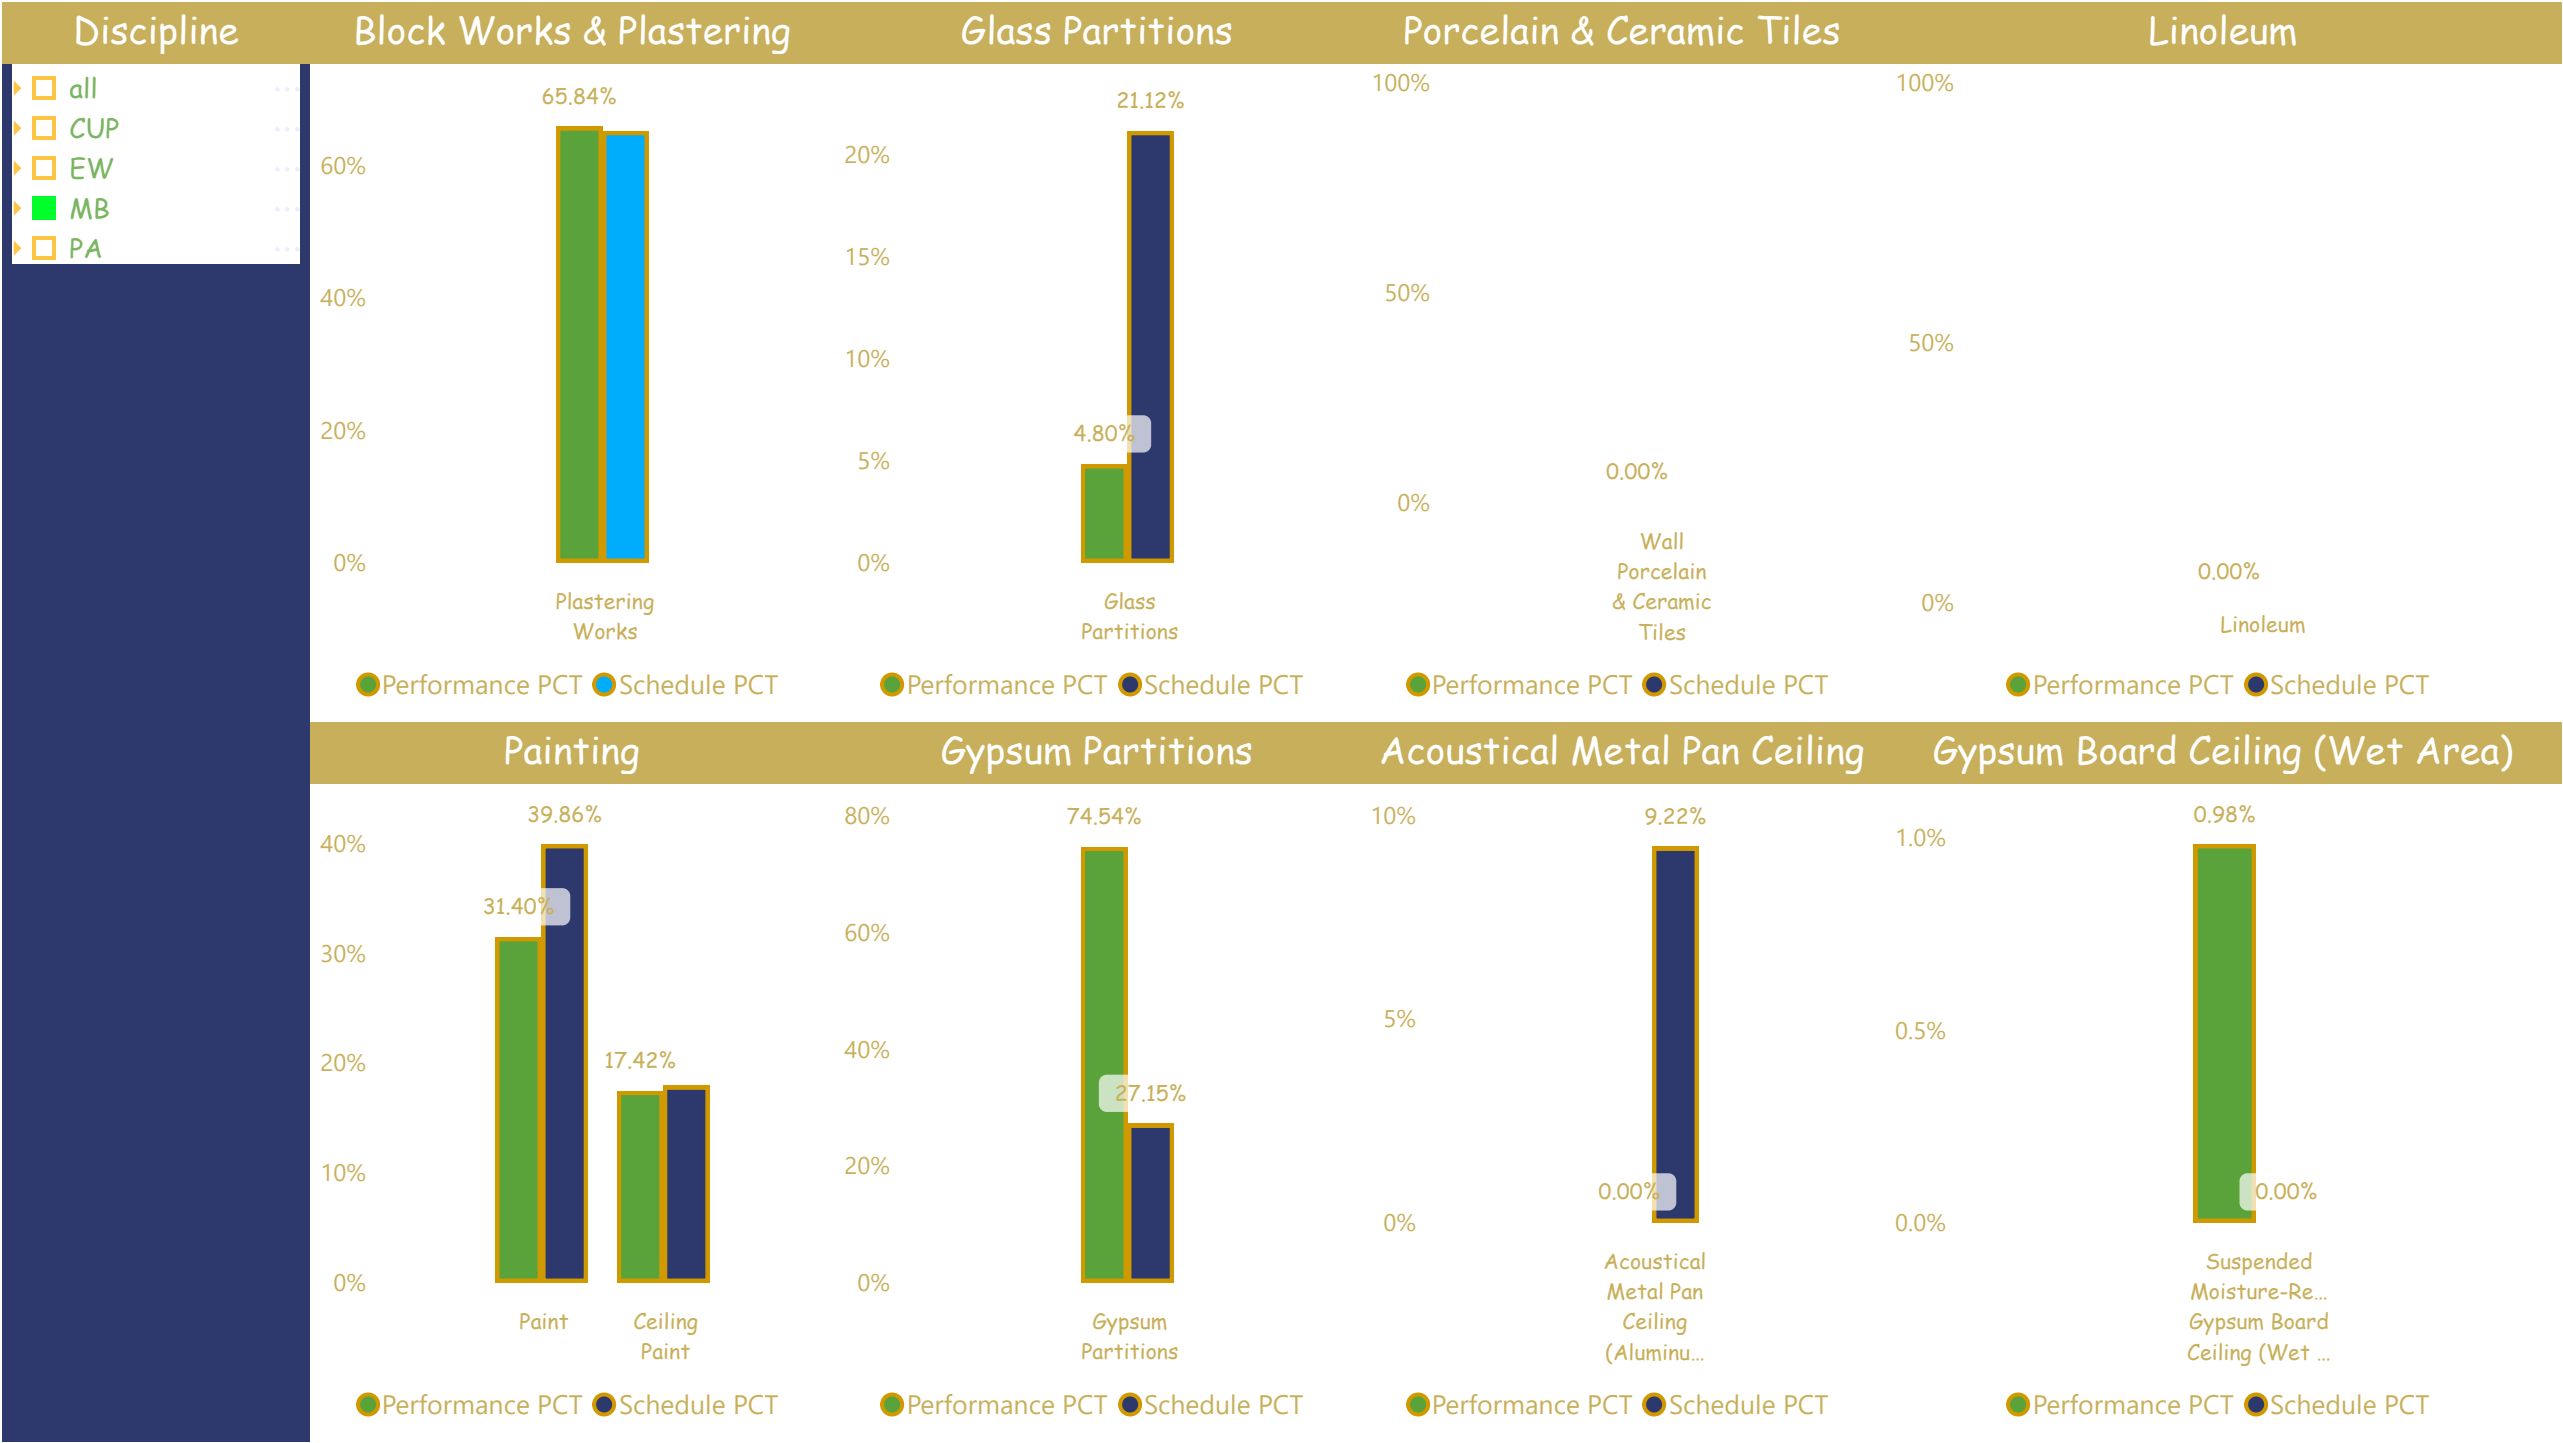



Discipline

Arch

Civil

ELE

Mech

Earned Value & Sch. Value

| 39.88M Sum of BCWS

40M

100%

0M

10M

20M

30M

40M

50M

60M

70M

80M

Activities Status

15.4%

22.43%

62.17%

TK_NotS...

TK_Com...

TK_Active

Perf. % Vs Sch. %

23.528%

23.528%

Earned Value Cost

40M

Planned Value Cost

40M

Budget Total Cost

170M

Navigator

Database.Cover Page

Database.Technical...

Database.Overall...

Database.Current...

Database.Curren...

Database.Current...

Database.Partial...

Database_Σ PV,EV,F...

Database_Σ PV,EV,F...

Database.Current...

Page 4

Page 5

Page 6

Progress Activities Trend

Activity ID	Activity Name	Activity Status
DA-C-CUP-GR-P-26-010	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B01-D-27-010	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B01-D-27-020	2nd Fix - Wiring	TK_Active
DA-C-M1-B01-P-26-010	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B01-P-26-020	2nd Fix - Wiring	TK_Active
DA-C-M1-B01-P-26-050	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B01-P-26-110	3rd Fix - Unit Fixture & Intial Testing	TK_Active
DA-C-M1-B01-P-27-020	2nd Fix - Wirina	TK_Active

SPI Partial by Date

0.88

1.00

1.00

1.00

1.01

Jan 2025

Jul 2025

Earned - Planned - Variance %

0.88%

-12.50%

-0.01%

-0.21%

-0.31%

Jan 2025

Jul 2025

Current Progress

Data Date	18-Sep-25
Budgeted Total Cost	169.50M
Earned Value Cost	39.88M
Planned Value Cost	39.88M
BL Project Start	05-Aug-24
BL Project Finish	07-Jul-26
Actual Start	15-Jul-24
Forecast Completion Date	11-Apr-26
Delay_Ahead (DB)	-63
Dealy/Ahead(Without Holiday)	-45
S.P.I	1.00
Elapsed_Days_DB	409
Remain Days (D)	320
Elapsed Time % (UP)	56.10%

EV & SV by Division

BCWP

BCWS

27M

13M

0M

0M

0M

D

C

Eng

S

P

BOQ

EV & SV by Discipline

BCWP

fBCWS

40M

ELE

DISCIPLINE

EV & SV by Building

BCWP

BCWS

27M

11M

1M

1M

all

MB

CUP

PA

BUILDING

EV & SV by Zone

BCWP

Sum of BCWS

27M

11M

1M

1M

all

Z1

Z3

Z2

ZONES

EV & SV by Work Type

BCWP

BCWS

27M

13M

0M

0M

0M

MD

Const

SU


AP

PO

WORK TYPE

OBIEDA OMARI


Sr. Planning

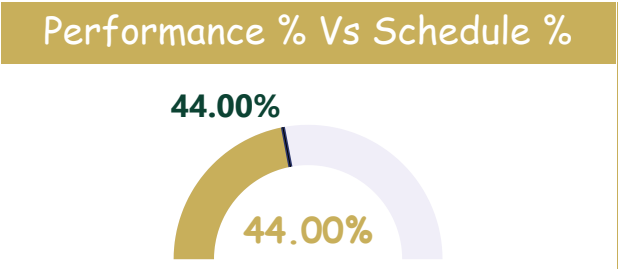


Current Progress

Data Date	18-Sep-25
Budgeted Total Cost	361.92M
Earned Value Cost	159.23M
Planned Value Cost	159.23M
BL Project Start	25-Jul-24
BL Project Finish	06-Jul-26
Actual Start	15-Jul-24
Forecast Completion Date	11-Apr-26
Delay_Ahead (DB)	-63
Dealy/Ahead(Without Holiday)	-45
S.P.I	1.00
Elapsed_Days_DB	420
Remain Days (D)	309
Elapsed Time % (UP)	57.61%

EV & SV by Division

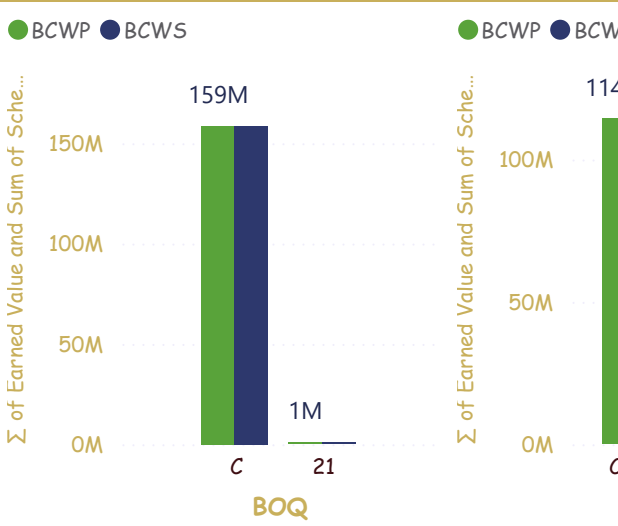

EV & SV by Discipline

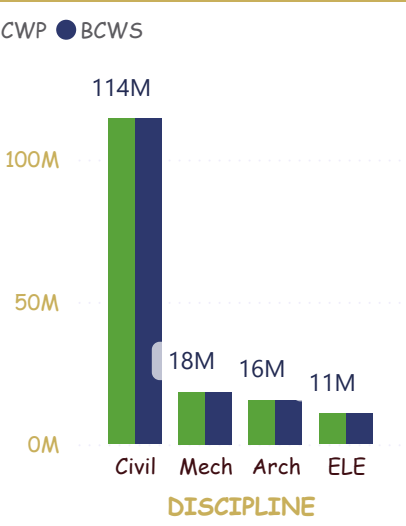


Project Break Down

- Z1
- Z2
- Z3


Construction Progress

FLOOR	Performance_%	Schedule_%
B2	83.81%	83.81%
B1	49.65%	49.65%
1st	43.28%	43.28%
GR	42.61%	42.61%
2nd	38.86%	38.86%
4th	36.60%	36.60%
5th	35.99%	35.99%
6th	29.61%	29.61%
3rd	27.16%	27.16%
RF	0.13%	0.13%
Total	44.00%	44.00%


EV & SV by Building

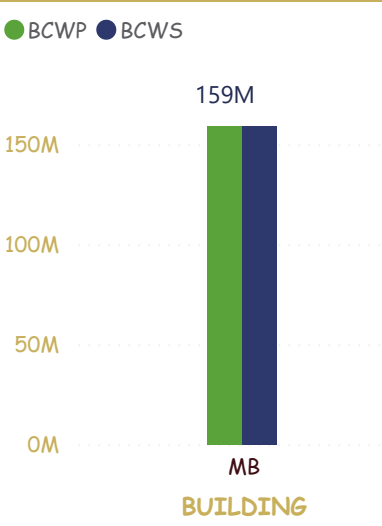



EV & SV by Zone

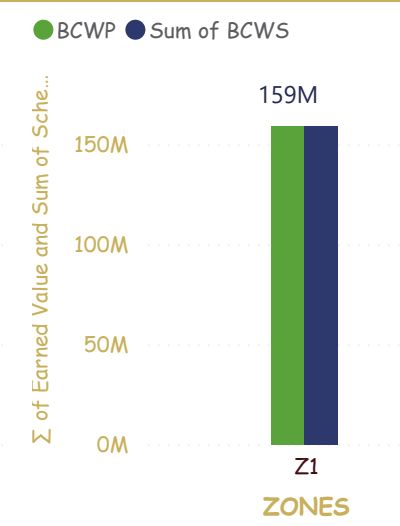

EV & SV by Work Type

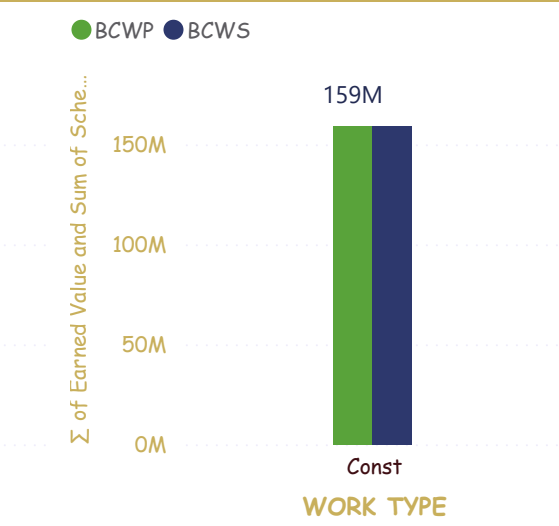

Activities Status

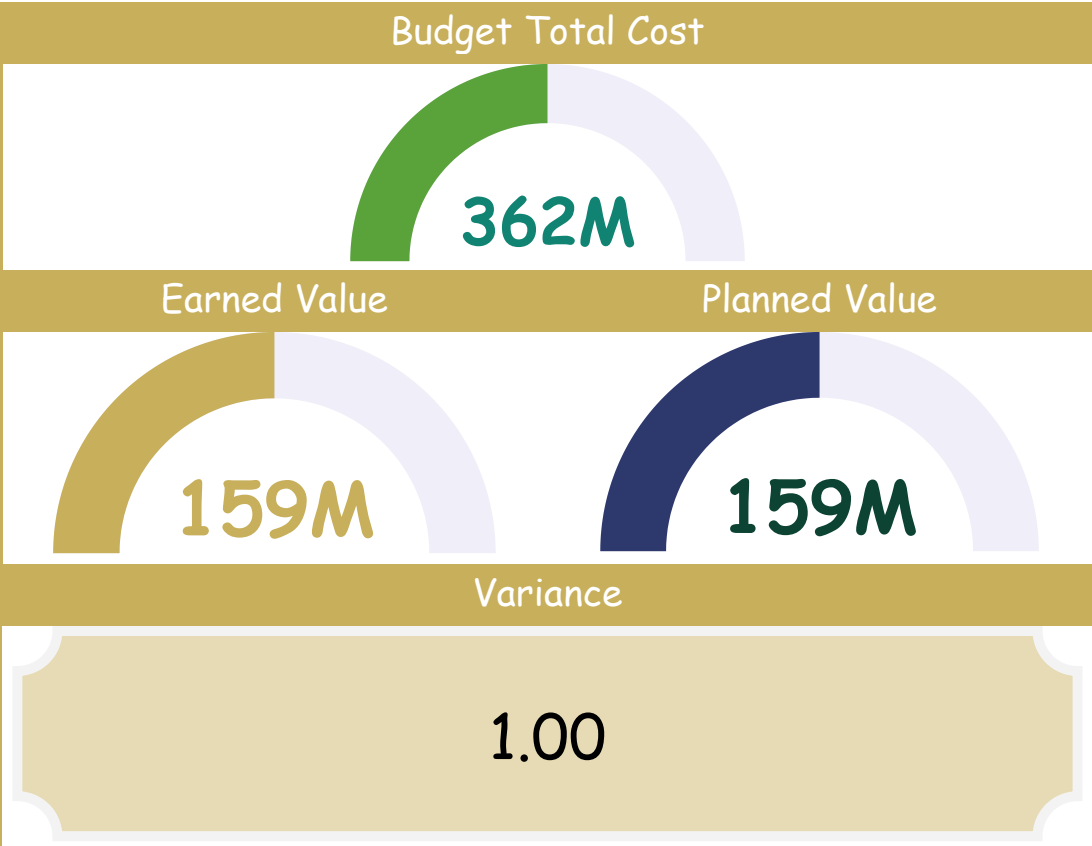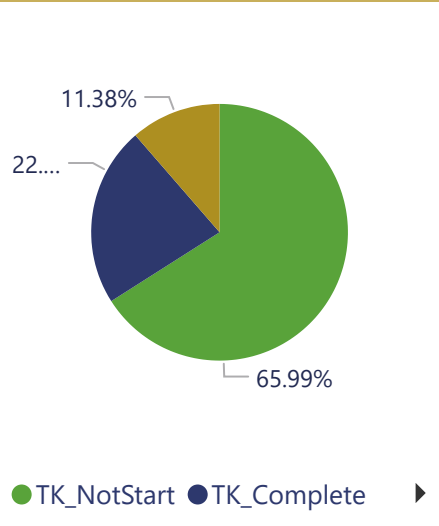

- Navigator
- Database.Cover Page
 - Database.Technical...
 - Database.Overall...
 - Database.Current...
 - Database.Current...
 - Database.Curren...
 - Database.Partial...
 - Database_Σ PV,EV,F...
 - Database_Σ PV,EV,F...
 - Database.Current...
 - Page 4
 - Page 5
 - Page 6



Project Break


Construction Progress

Planned, Earned, Forecast S-Curve

Navigator


- Down
- WBS: MB
- ▶ ○ CUP
- ▶ ● MB
- ▶ ○ PA

FLOOR	Performance_%	Schedule_%
B2	32.27%	32.27%
2nd	19.71%	19.71%
4th	19.69%	19.69%
5th	18.75%	18.75%
B1	17.71%	17.71%
6th	13.44%	13.44%
GR	13.11%	13.11%
1st	11.04%	11.04%
3rd	6.77%	6.77%
Total	15.54%	15.54%

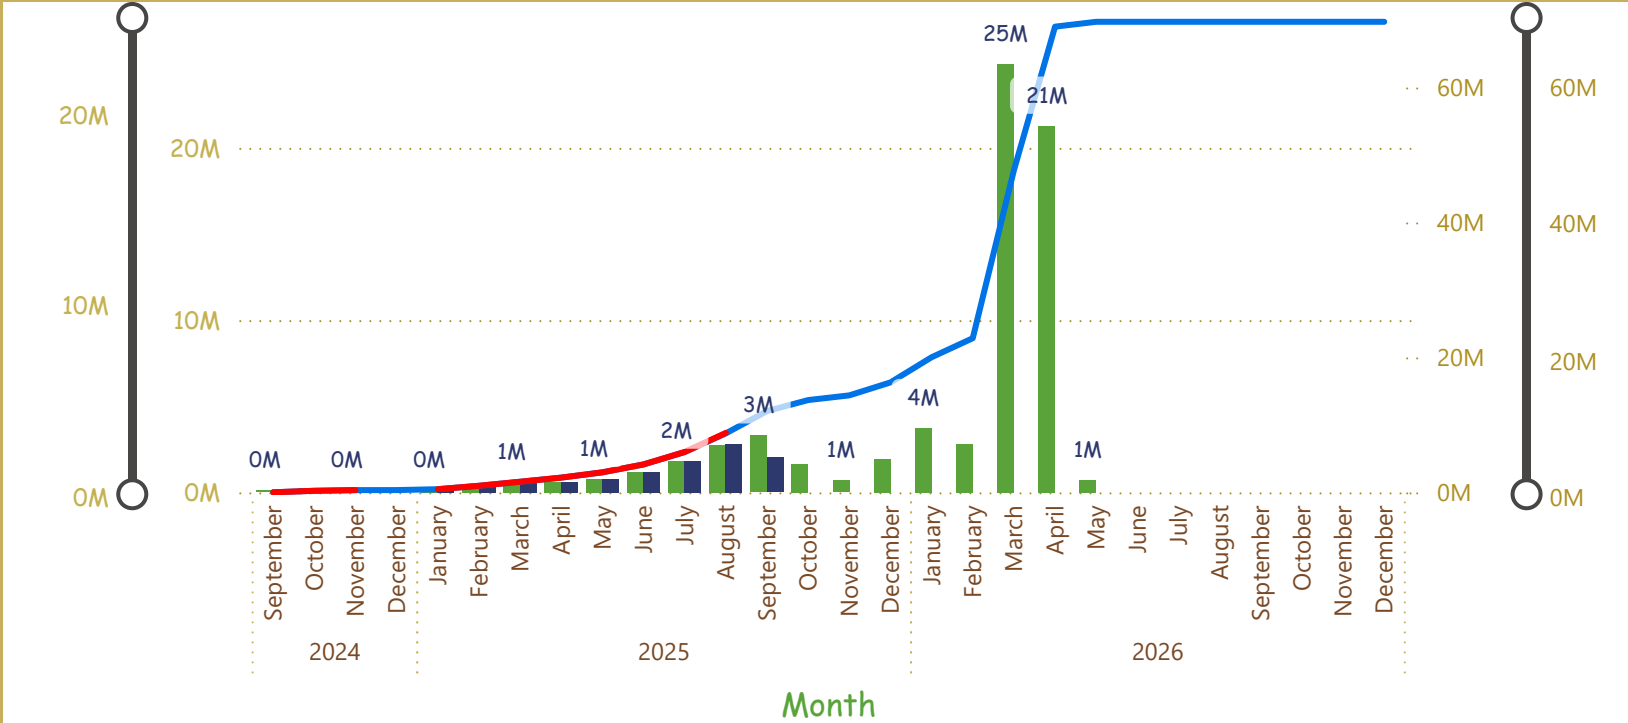

- Database.Cover Page
- Database.Technical...
- Database.Overall...
- Database.Current...
- Database.Current...
- Database.Current...
- Database.Current...
- Database.Partial..
- Database.Σ PV,EV,F...
- Database.Σ PV,EV,F...

- Project Break
- Down
- WBS: ELE
- Arch
- Civil
- ELE
- Mech

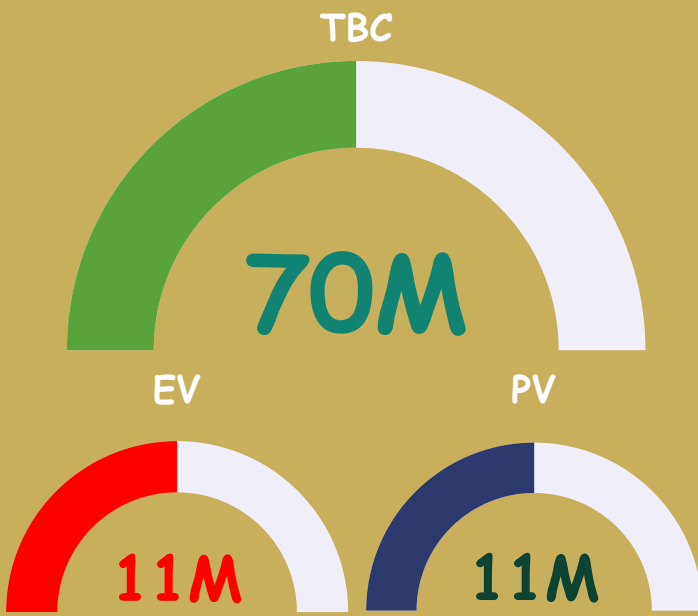

Progress Activities Trend

Activity ID	Activity Name	Activity Status
DA-C-M1-B01-D-27-010	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B01-D-27-020	2nd Fix - Wiring	TK_Active
DA-C-M1-B01-P-26-010	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B01-P-26-020	2nd Fix - Wiring	TK_Active
DA-C-M1-B01-P-26-050	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B01-P-26-110	3rd Fix - Unit Fixture & Intial Testing	TK_Active
DA-C-M1-B01-P-27-020	2nd Fix - Wiring	TK_Active
DA-C-M1-B02-F-28-030	3rd Fix - Unit Fixture & Intial Testing	TK_Active
DA-C-M1-B02-P-26-020	2nd Fix - Wiring	TK_Active
DA-C-M1-B02-P-26-050	1st Fix - Pipes & Boxes Installation	TK_Active
DA-C-M1-B02-P-26-110	3rd Fix - Unit Fixture & Intial Testing	TK_Active
DA-C-M1-B02-P-27-020	2nd Fix - Wiring	TK_Active
DA-C-M1-GR-D-27-020	2nd Fix - Wiring	TK_Active
DA-C-M1-GR-F-28-030	3rd Fix - Unit Fixture & Intial Testing	TK_Active
DA-C-M1-GR-P-26-020	2nd Fix - Wiring	TK_Active
DA-C-M1-GR-P-26-050	1st Fix - Pipes & Boxes Installation	TK_Active

- Database.Σ PV,EV,F...
- Database.Σ PV,EV,F...
- Database.Current...
- Page 4
- Page 5
- Page 6



Level

1st

2nd

3rd

4th

5th

6th

All

B1

B2

EX

GR

DE

all

CUP

MB

Zone

Z1

Z3

Discipline

Arch

Civil

ELE

Mech

Current Progress

Data Date

18-Sep-25

Budgeted Total Cost

26.53M

Earned Value Cost

3.54M

Planned Value Cost

3.54M

BL Project Start

27-Oct-24

BL Project Finish

23-Jun-26

Actual Start

15-Jul-24

Forecast Completion Date

21-Feb-26

Delay_Ahead (DB)

-84

Dealy/Ahead(Without Holiday)

-60

S.P.I

1.00

Elapsed_Days_DB

326

Remain Days (D)

403

Elapsed Time % (UP)

44.72%

Work Breakdown Structure - Total Float Status

WBS_NAME	Total Float
Furnishings	-118
Signage Enlarged Details	-118
Signage Plans	-118
Doors & Windows	-117
Ceiling	-115
Specialties	-114
Metals	-113
Thermal Work	-112
Finishes Schedule	-110
PATTERN PLAN	-110
Metal Doors	-54
Porcelain & Ceramic Tiles	-48
Suspended Moisture-Resistant Gypsum Board Ceiling (Wet Area)	-46
Wall Porcelain & Ceramic Tiles	-46
Glass Partitions	-45
Cabinats	-42
Curtain	-42
Decoration VE Glass Screen	-42
Paint	-42
Signages	-40
Linoleum	-37
Wooden Benches	-36
Access Panel Doors	-35
Wooden Doors	-35
Epoxy	-34
Toilet Accessories	-34
Aluminum Windows	-33
Acoustical Metal Pan Ceiling (Aluminum Tiles)	-31
Phenolic-Core Toilet Partition (Wet Area)	-31
Ceiling Paint	-24
Counters	-24
HDF (High-Density Fiberboard) Cladding	-21
Wall Epoxy Paint	-19
3D Decorative PVC Cladding	-17
Fire Extinguishers	-16

Database.Cover Page

Database.Technical...

Database.Overall...

Database.Current...

Database.Current...

Database.Current...

Database.Partial...

Database.Σ PV,EV,F...

Database.Σ PV,EV,F...

Database.Curren...

Page 4

Page 5


Page 6

OBIEDA OMARI

SR. PLANNING

Planned, Earned, Forecast S-Curve

Navigator

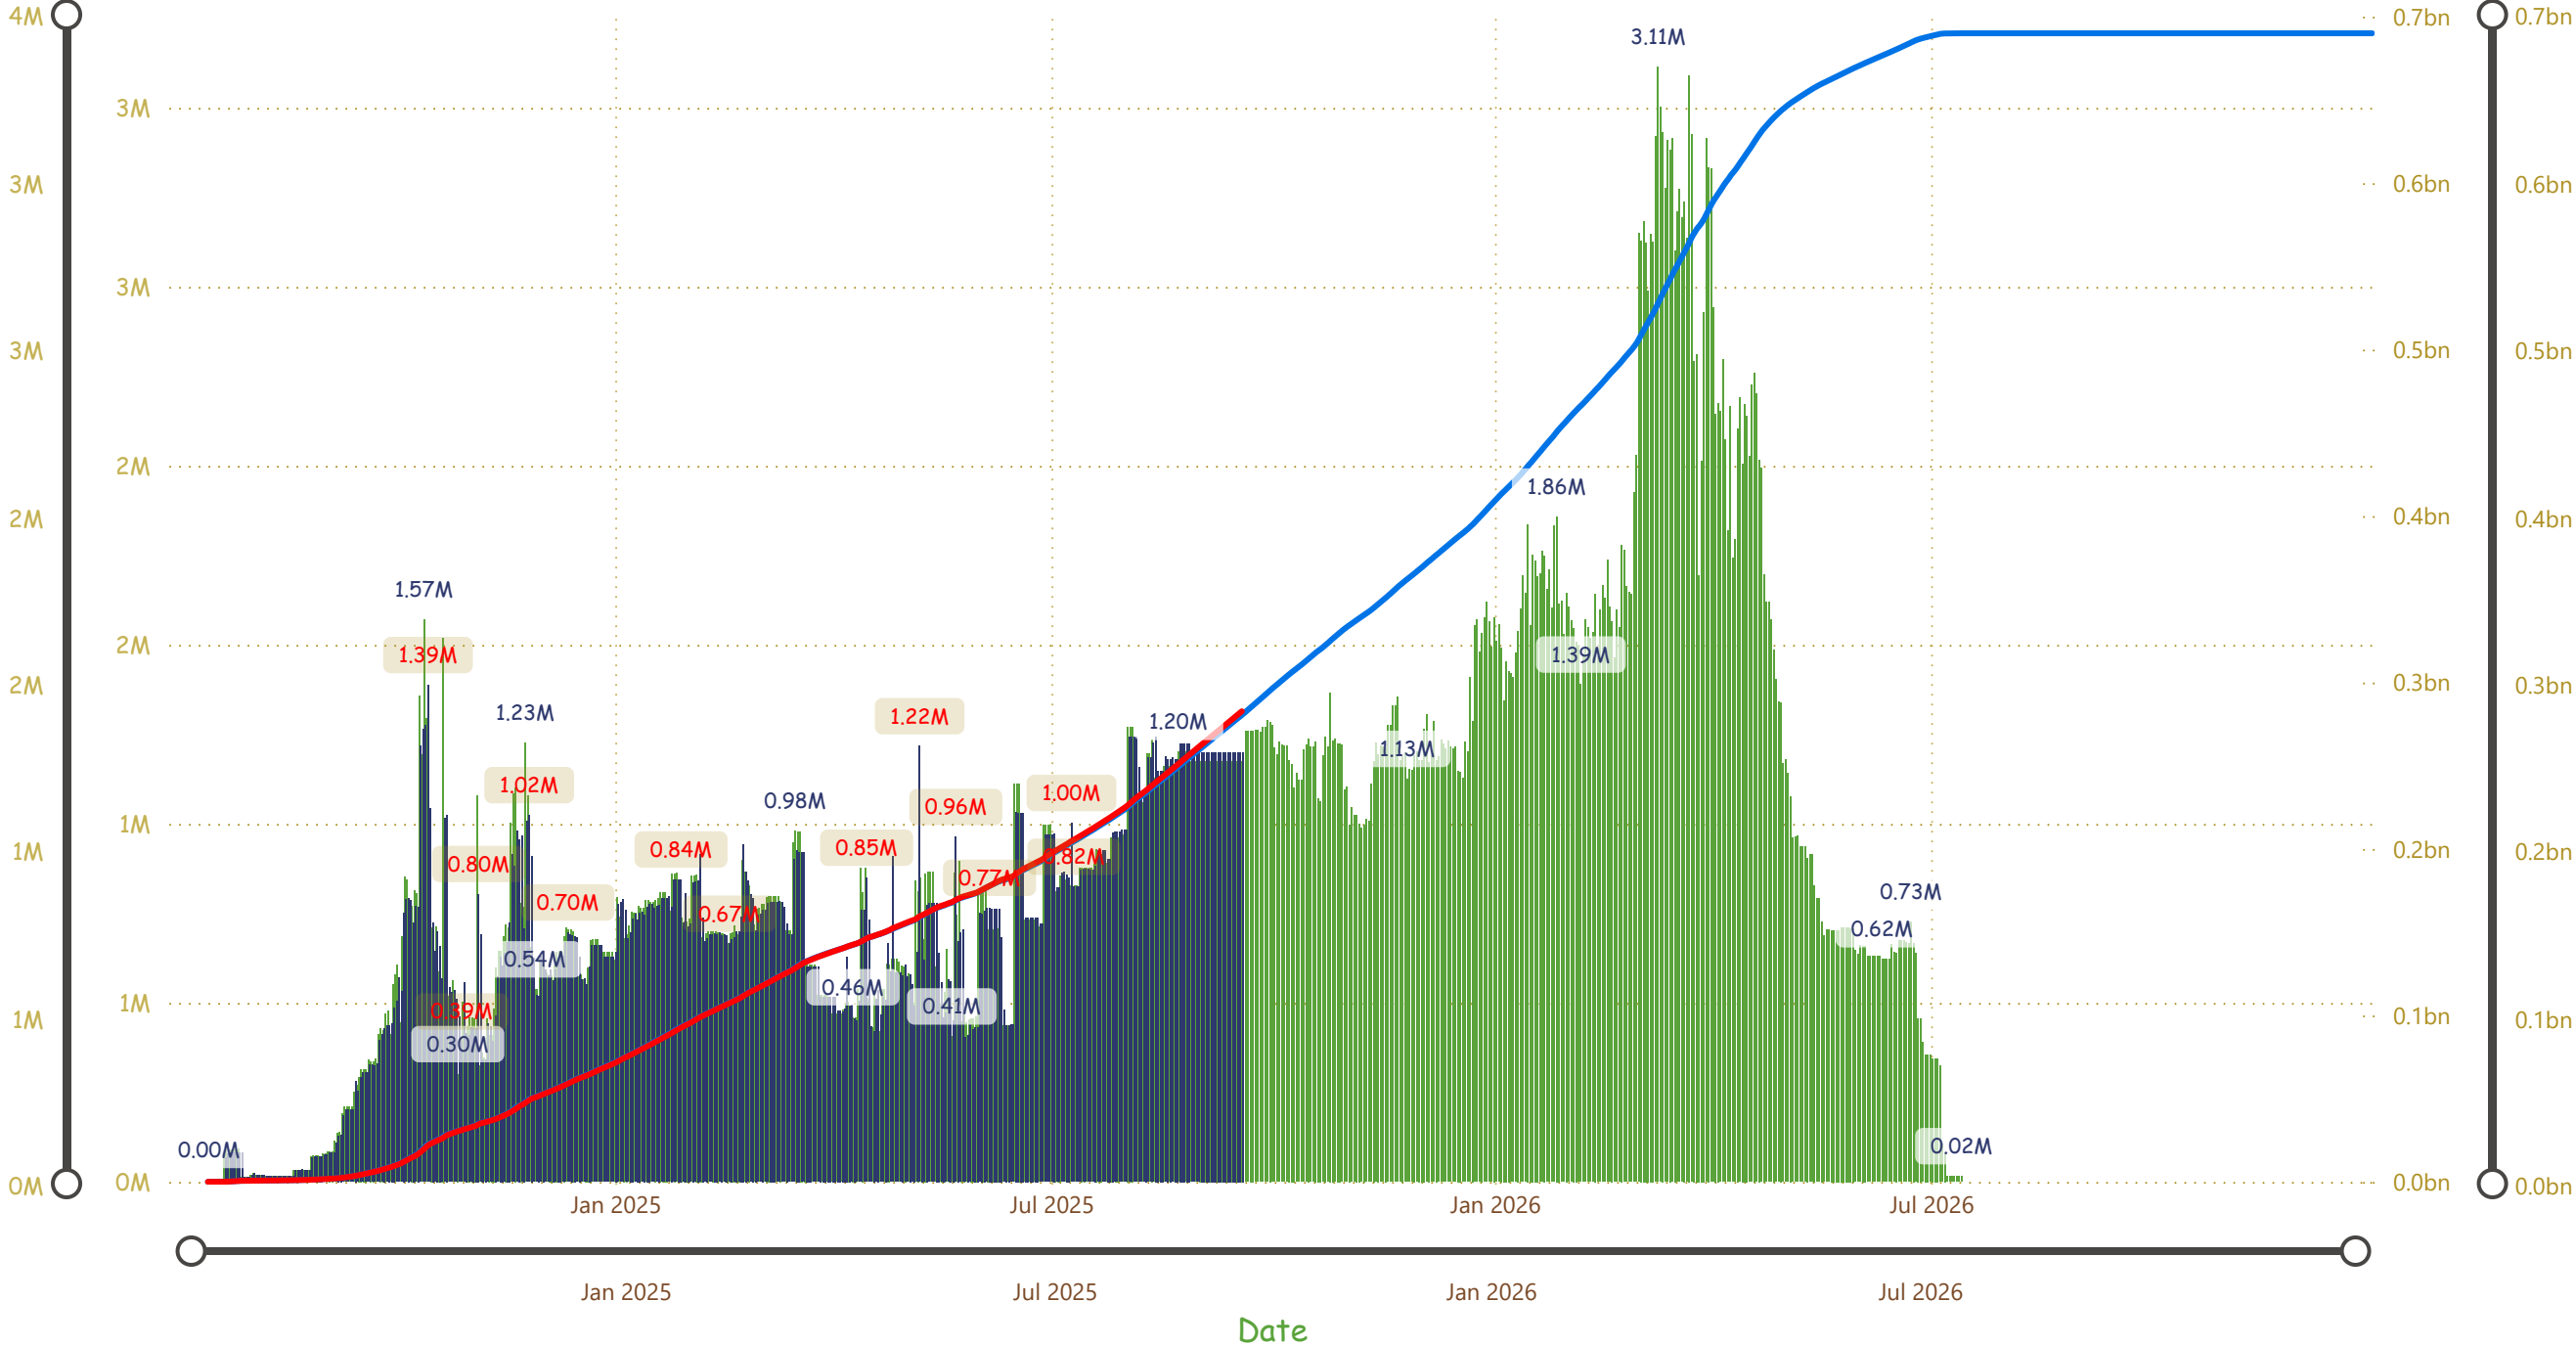

Database.Cover Page

Database.Technical...

Database.Overall...

Database.Current...

Database.Current...

Database.Current...

Database.Current...

Database.Partial...

Database.Σ PV,EV,F...

Database.Σ...

Database.Current...

Page 4

Page 5

Page 6

